

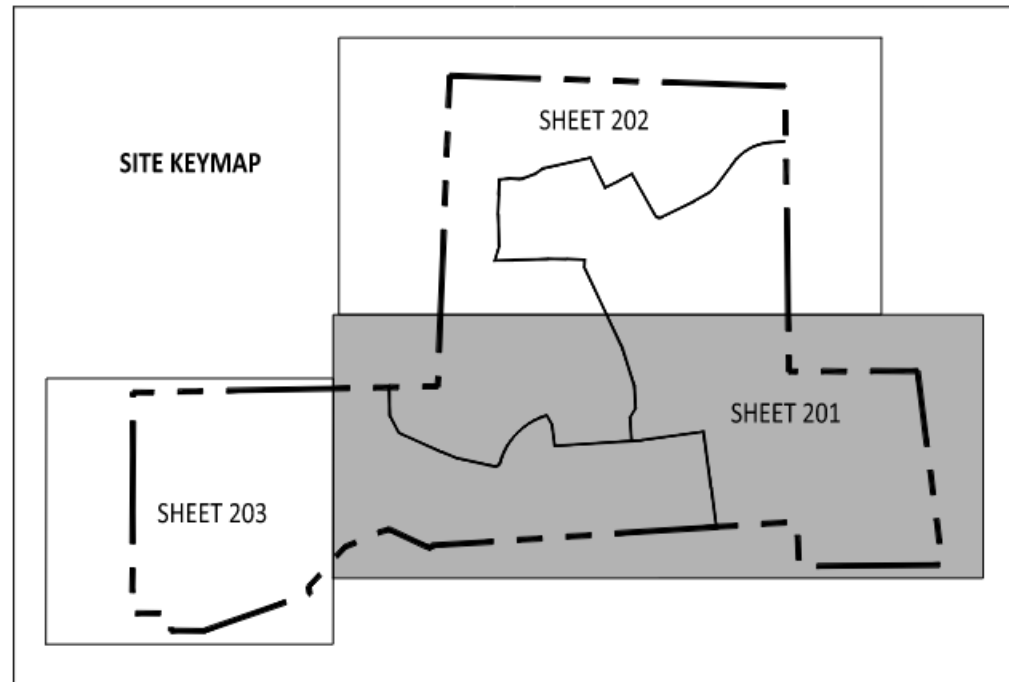


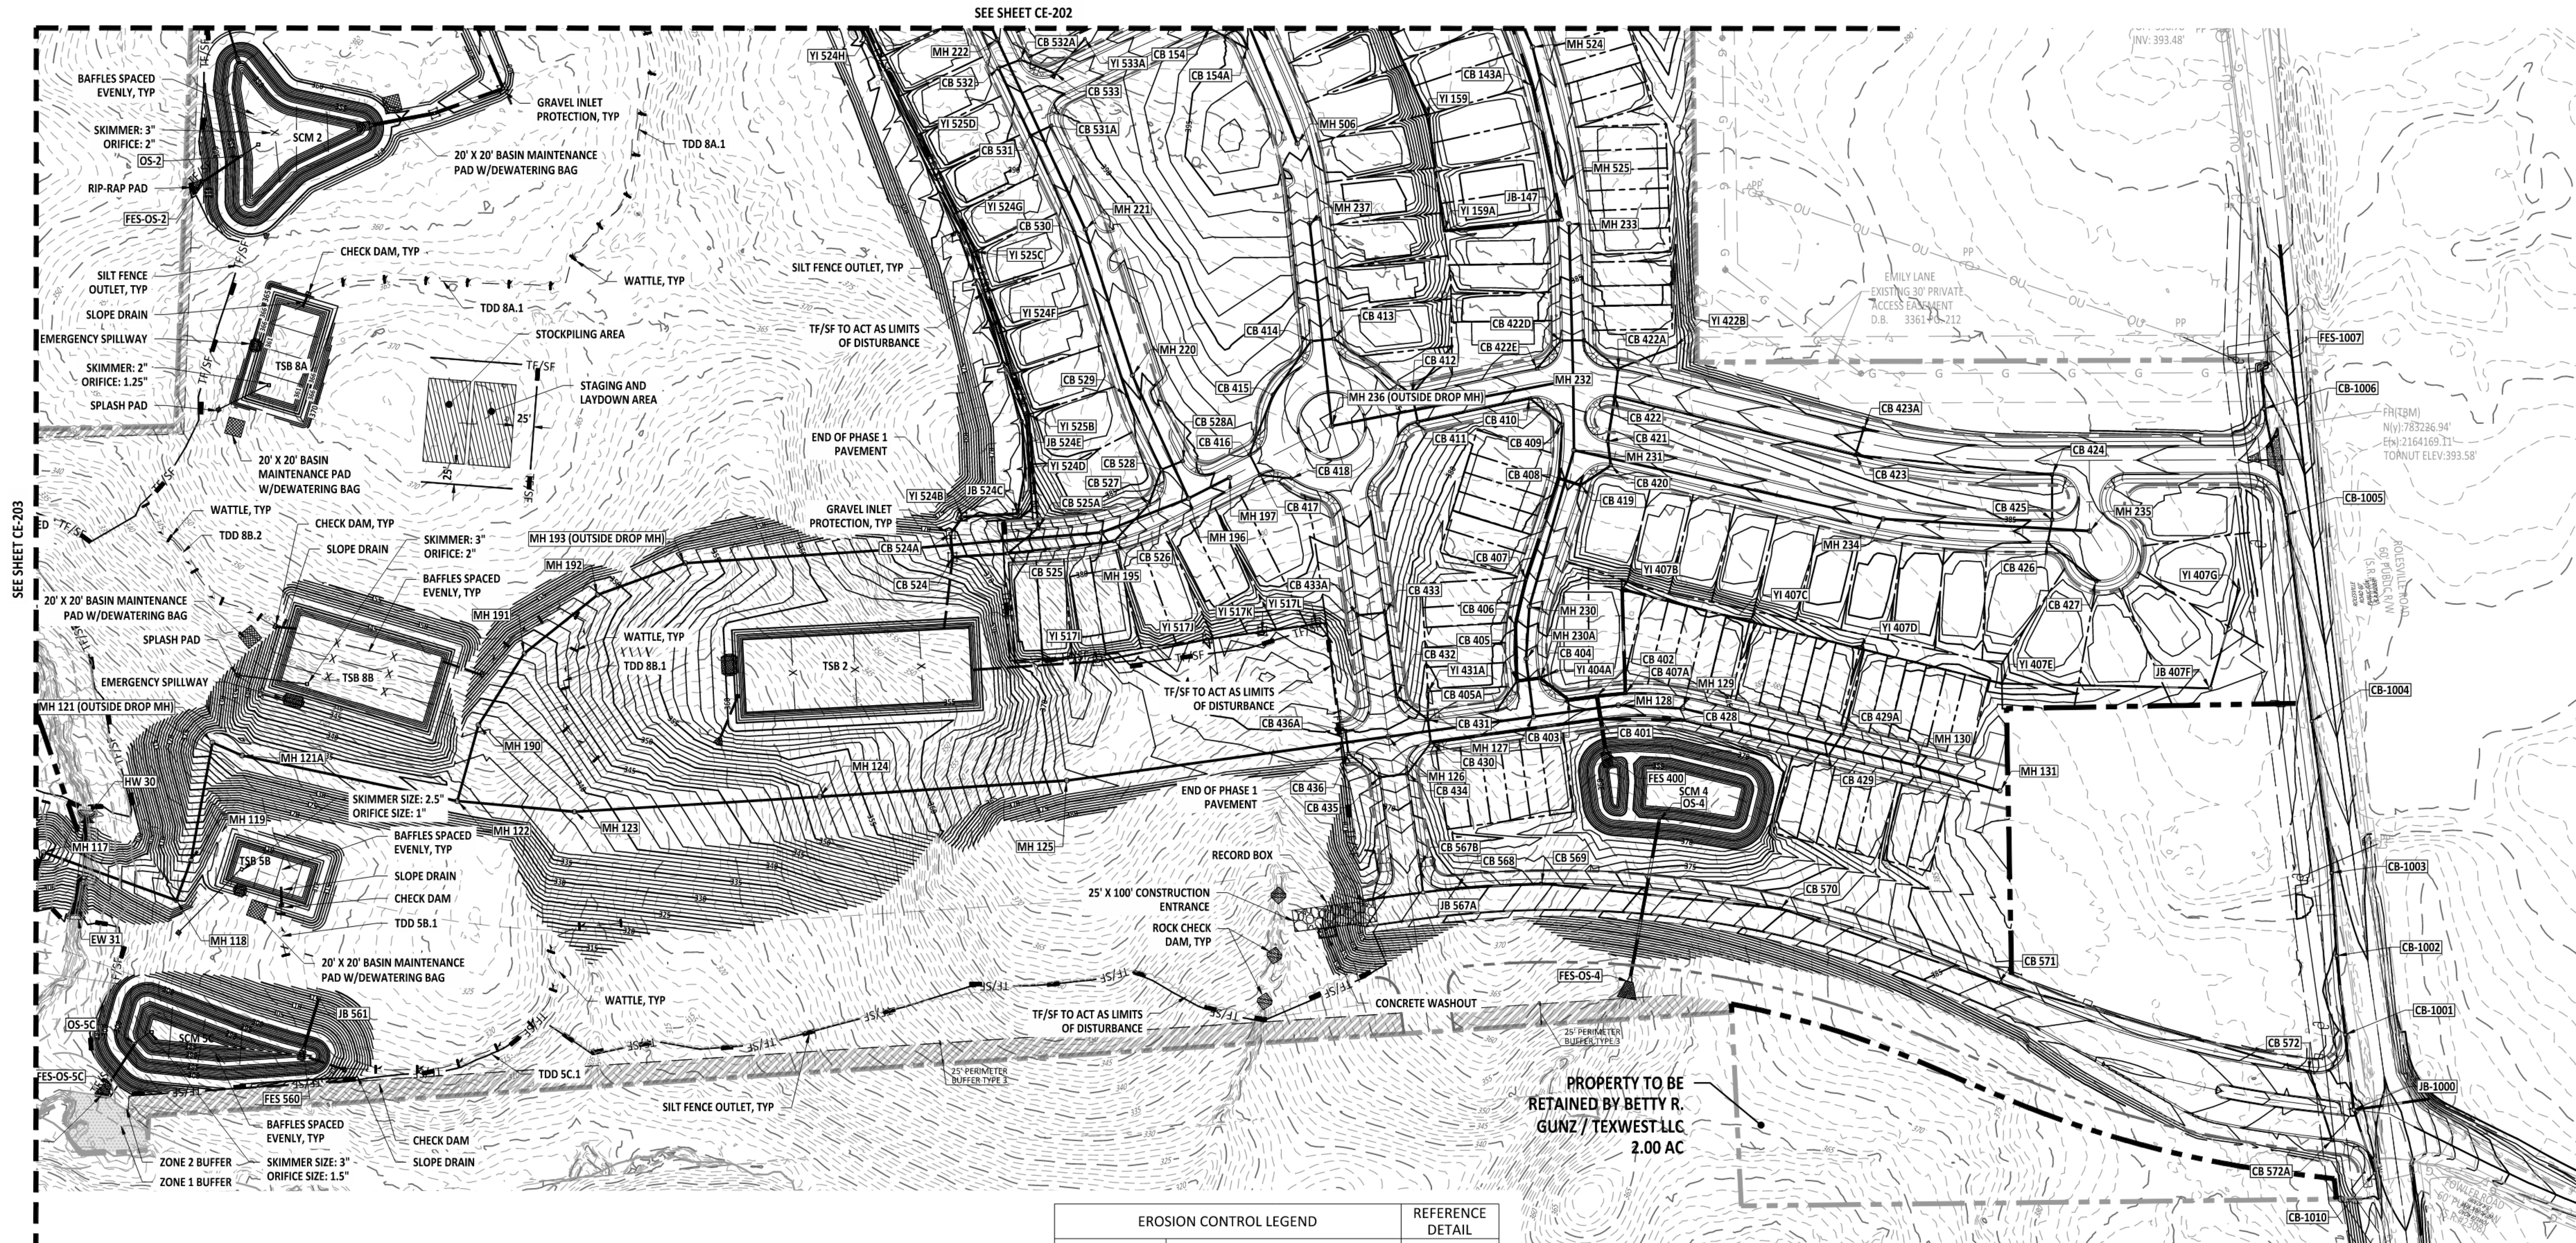

EROSION CONTROL LEGEND		REFERENCE DETAIL
TF/SF	SILT FENCE/TREE PROTECTION FENCE COMBO (LOD)	01 / CE501
LOD	LIMITS OF DISTURBANCE	SEE PLANS
TF	TREE PROTECTION FENCE (LOD)	08 / CE502
—>—>	TEMPORARY DIVERSION DITCH	06 / CE500 & CE504
X	BAFFLE	05 / CE501
■	SILT FENCE OUTLET	02 / CE501
●	SEDIMENT SACK INLET PROTECTION	03 / CE501
⌋	STANDARD PIPE INLET PROTECTION	08 / CE501
⌋	GRAVEL INLET PROTECTION	04 / CE500
⌋	GRAVEL CHECK DAM	03 / CE500
⌋	MAINTENANCE PAD	06 / CE502
⌋	RIPRAP DISSIPATOR	07 & 08 / CE500
—>—>	SLOPE DRAIN/DRAINAGE PIPE	09 / CE500
—	WATTLE	05 / CE500
□	SKIMMER	01 / CE502
⌋	TEMPORARY SKIMMER BASIN	05 & 06 / CE501
⌋	STAGING AND LAYDOWN AREA	NCG01 / CE503
⌋	CONSTRUCTION ENTRANCE	02 / CE500
⌋	CONCRETE WASHOUT PIT	NCG01 / CE503
⌋	BRIDGE MAT	03 / CE502
⌋	FUTURE PHASE 2 & 3	N/A

SITE LEGEND	
---	PROPERTY BOUNDARY
---	NEUSE RIVER BUFFER ZONE 1
---	NEUSE RIVER BUFFER ZONE 2
---	LIMITS OF DISTURBANCE
---	WETLANDS

- GENERAL NOTES:
- ROLLED EROSION CONTROL PRODUCT (RECP) SHALL BE INSTALLED WHERE THE DIFFERENCE IN ELEVATION IS GREATER THAN 10 FT, WITHIN BASINS, AND WHERE SLOPES ARE GREATER THAN 3:1.
 - SEE SHEET G-005 FOR TEMPORARY DIVERSION DITCH (TDD) AND SLOPE DRAIN SIZING SCHEDULE.

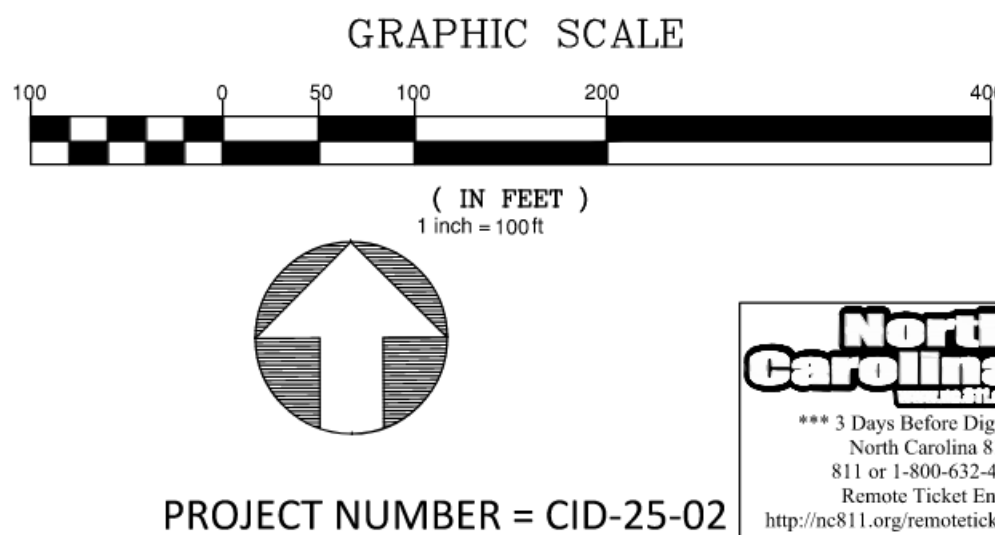

NO.	DATE	REVISION

STIPULATION FOR REUSE

THIS DRAWING WAS PREPARED FOR USE ON THE SPECIFIC SITE, NAMED HEREON, CONTEMPORANEOUSLY WITH ITS ISSUE DATE AS LISTED, HEREON, AND IT IS NOT SUITABLE FOR USE ON A DIFFERENT PROJECT SITE OR AT A LATER TIME. USE OF THIS DRAWING FOR REFERENCE OR EXAMPLE ON ANOTHER PROJECT REQUIRES THE SERVICES OF PROPERLY LICENSED ARCHITECTS AND ENGINEERS. REPRODUCTION OF THIS DRAWING FOR REUSE ON ANOTHER PROJECT IS NOT AUTHORIZED AND MAY BE CONTRARY TO THE LAW.

MERRITT RESERVE
EROSION CONTROL
PHASE 2 & 3 STAGE 1
ROLESVILLE RD
WAKE COUNTY NC 27312

JOB NUMBER: 23-0004
CHECKED BY: JK
DRAWN BY: DH/MA/LL
DATE: 12/12/2025

SHEET TITLE:
EROSION CONTROL PHASE 2 & 3 STAGE 1
SHEET NO.:
CE-201



1. ROLLED EROSION CONTROL PRODUCT (RECP) SHALL BE INSTALLED WHERE THE DIFFERENCE IN ELEVATION IS GREATER THAN 10 FT, WITHIN BASINS, AND WHERE SLOPES ARE GREATER THAN 3:1.
2. SEE SHEET G-005 FOR TEMPORARY DIVERSION DITCH (TDD) AND SLOPE DRAIN SIZING SCHEDULE.



—

1




GRAPHIC SCALE

(IN FEET
1 inch = 100 ft

1 inch = 100 ft

PROJECT NUMBER = CID-25-02



*** 3 Days Before Digging
North Carolina 811
811 or 1-800-632-4949
Remote Ticket Entry
<http://nc811.org/remotetickets>

JOB NUMBER: 23 0004

JOB NUMBER. 23-0004

DRAWN BY: DH/MA/LL

DATE: 12/12/2025

**EROSION
CONTROL PHASE
2 & 3 STAGE 1**

SHEET NO. :

CE-202



Digitally signed by
Jakob Klein
Date: 2026.01.09




NO.	DATE	REVISION:
-----	------	-----------

STIPULATION FOR REUSE

THIS DRAWING WAS PREPARED FOR USE ON THE SPECIFIC SITE, NAMED HEREON, CONTEMPORANEOUSLY WITH ITS ISSUE DATE AS LISTED, HEREON. AND IT IS NOT SUITABLE FOR USE ON A DIFFERENT PROJECT SITE OR AT A LATER TIME. USE OF THIS DRAWING FOR REFERENCE OR EXAMPLE ON ANOTHER PROJECT REQUIRES THE SERVICES OF PROPERLY LICENSED ARCHITECTS AND ENGINEERS. REPRODUCTION OF THIS DRAWING FOR REUSE ON ANOTHER PROJECT IS NOT AUTHORIZED AND MAY BE CONTRARY TO THE LAW.




GRAPHIC SCALE



The graphic scale bar is a horizontal line with alternating black and white segments. It is marked with numbers 100, 0, 50, 100, 200, and 400. Below the bar, the text "(IN FEET)" is centered, followed by "1 inch = 100ft". Below the scale bar is a circular north arrow with a white arrow pointing upwards and a shaded circular border.

SITE LEGEND	
	PROPERTY BOUNDARY
	NEUSE RIVER BUFFER ZONE 1
	NEUSE RIVER BUFFER ZONE 2
	LIMITS OF DISTURBANCE
	WETLANDS

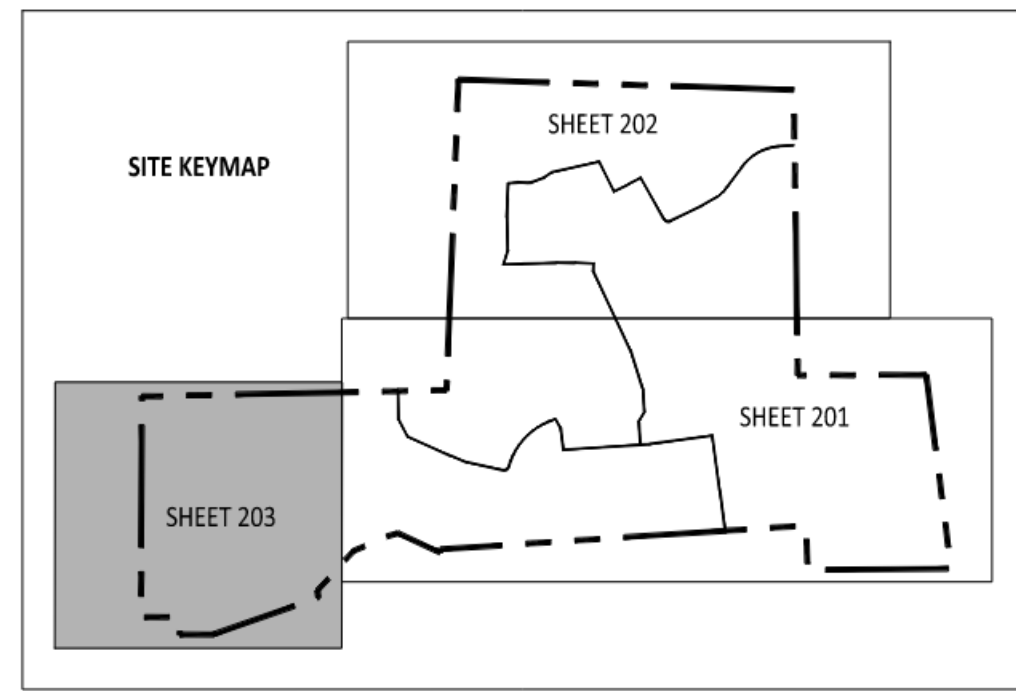[illegible]

STIPULATION FOR REUSE

THIS DRAWING WAS PREPARED FOR USE ON THE SPECIFIC SITE, NAMED HEREON, CONTEMPORANEOUSLY WITH ITS ISSUE DATE AS LISTED, HEREON, AND IT IS NOT SUITABLE FOR USE ON A DIFFERENT PROJECT SITE OR AT A LATER TIME. USE OF THIS DRAWING FOR REFERENCE OR EXAMPLE ON ANOTHER PROJECT REQUIRES THE SERVICES OF PROPERLY LICENSED ARCHITECTS AND ENGINEERS. REPRODUCTION OF THIS DRAWING FOR REUSE ON ANOTHER PROJECT IS NOT AUTHORIZED AND MAY BE CONTRARY TO THE LAW.

**MERRITT RESERVE
EROSION CONTROL
PHASE 2 & 3 STAGE 1**
ROLESVILLE RD
WAKE COUNTY NC 27312



JOB NUMBER:	23-0004
CHECKED BY:	JK
DRAWN BY:	DH/MA/LL
DATE:	12/12/2025








**EROSION
CONTROL PHASE
2 & 3 STAGE 1**

SHEET NO.: **CE-203**



PROJECT NUMBER = CID-25-02

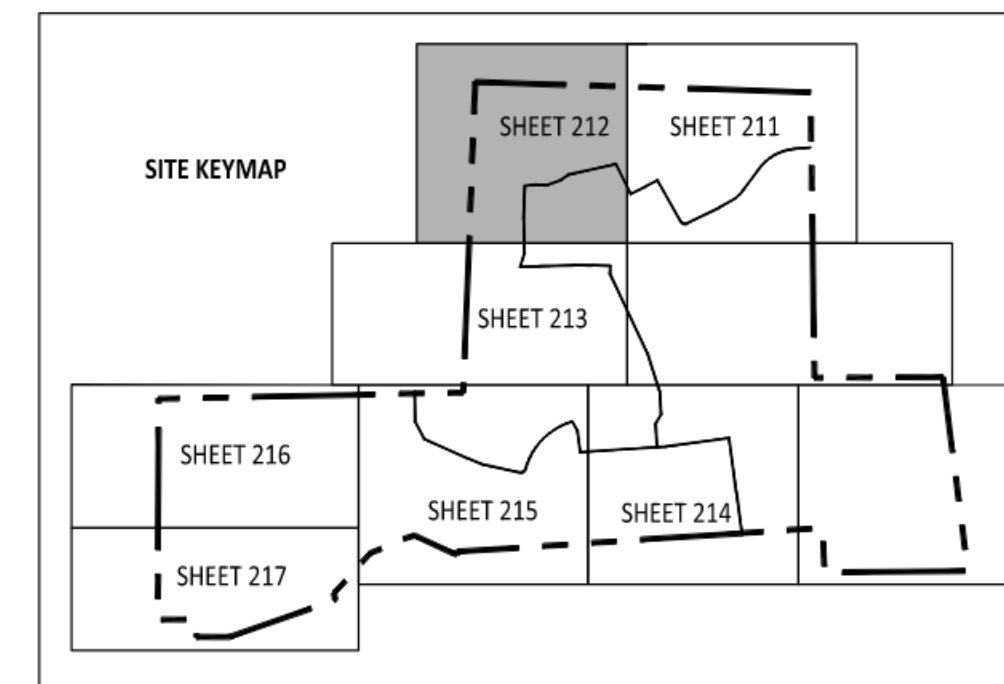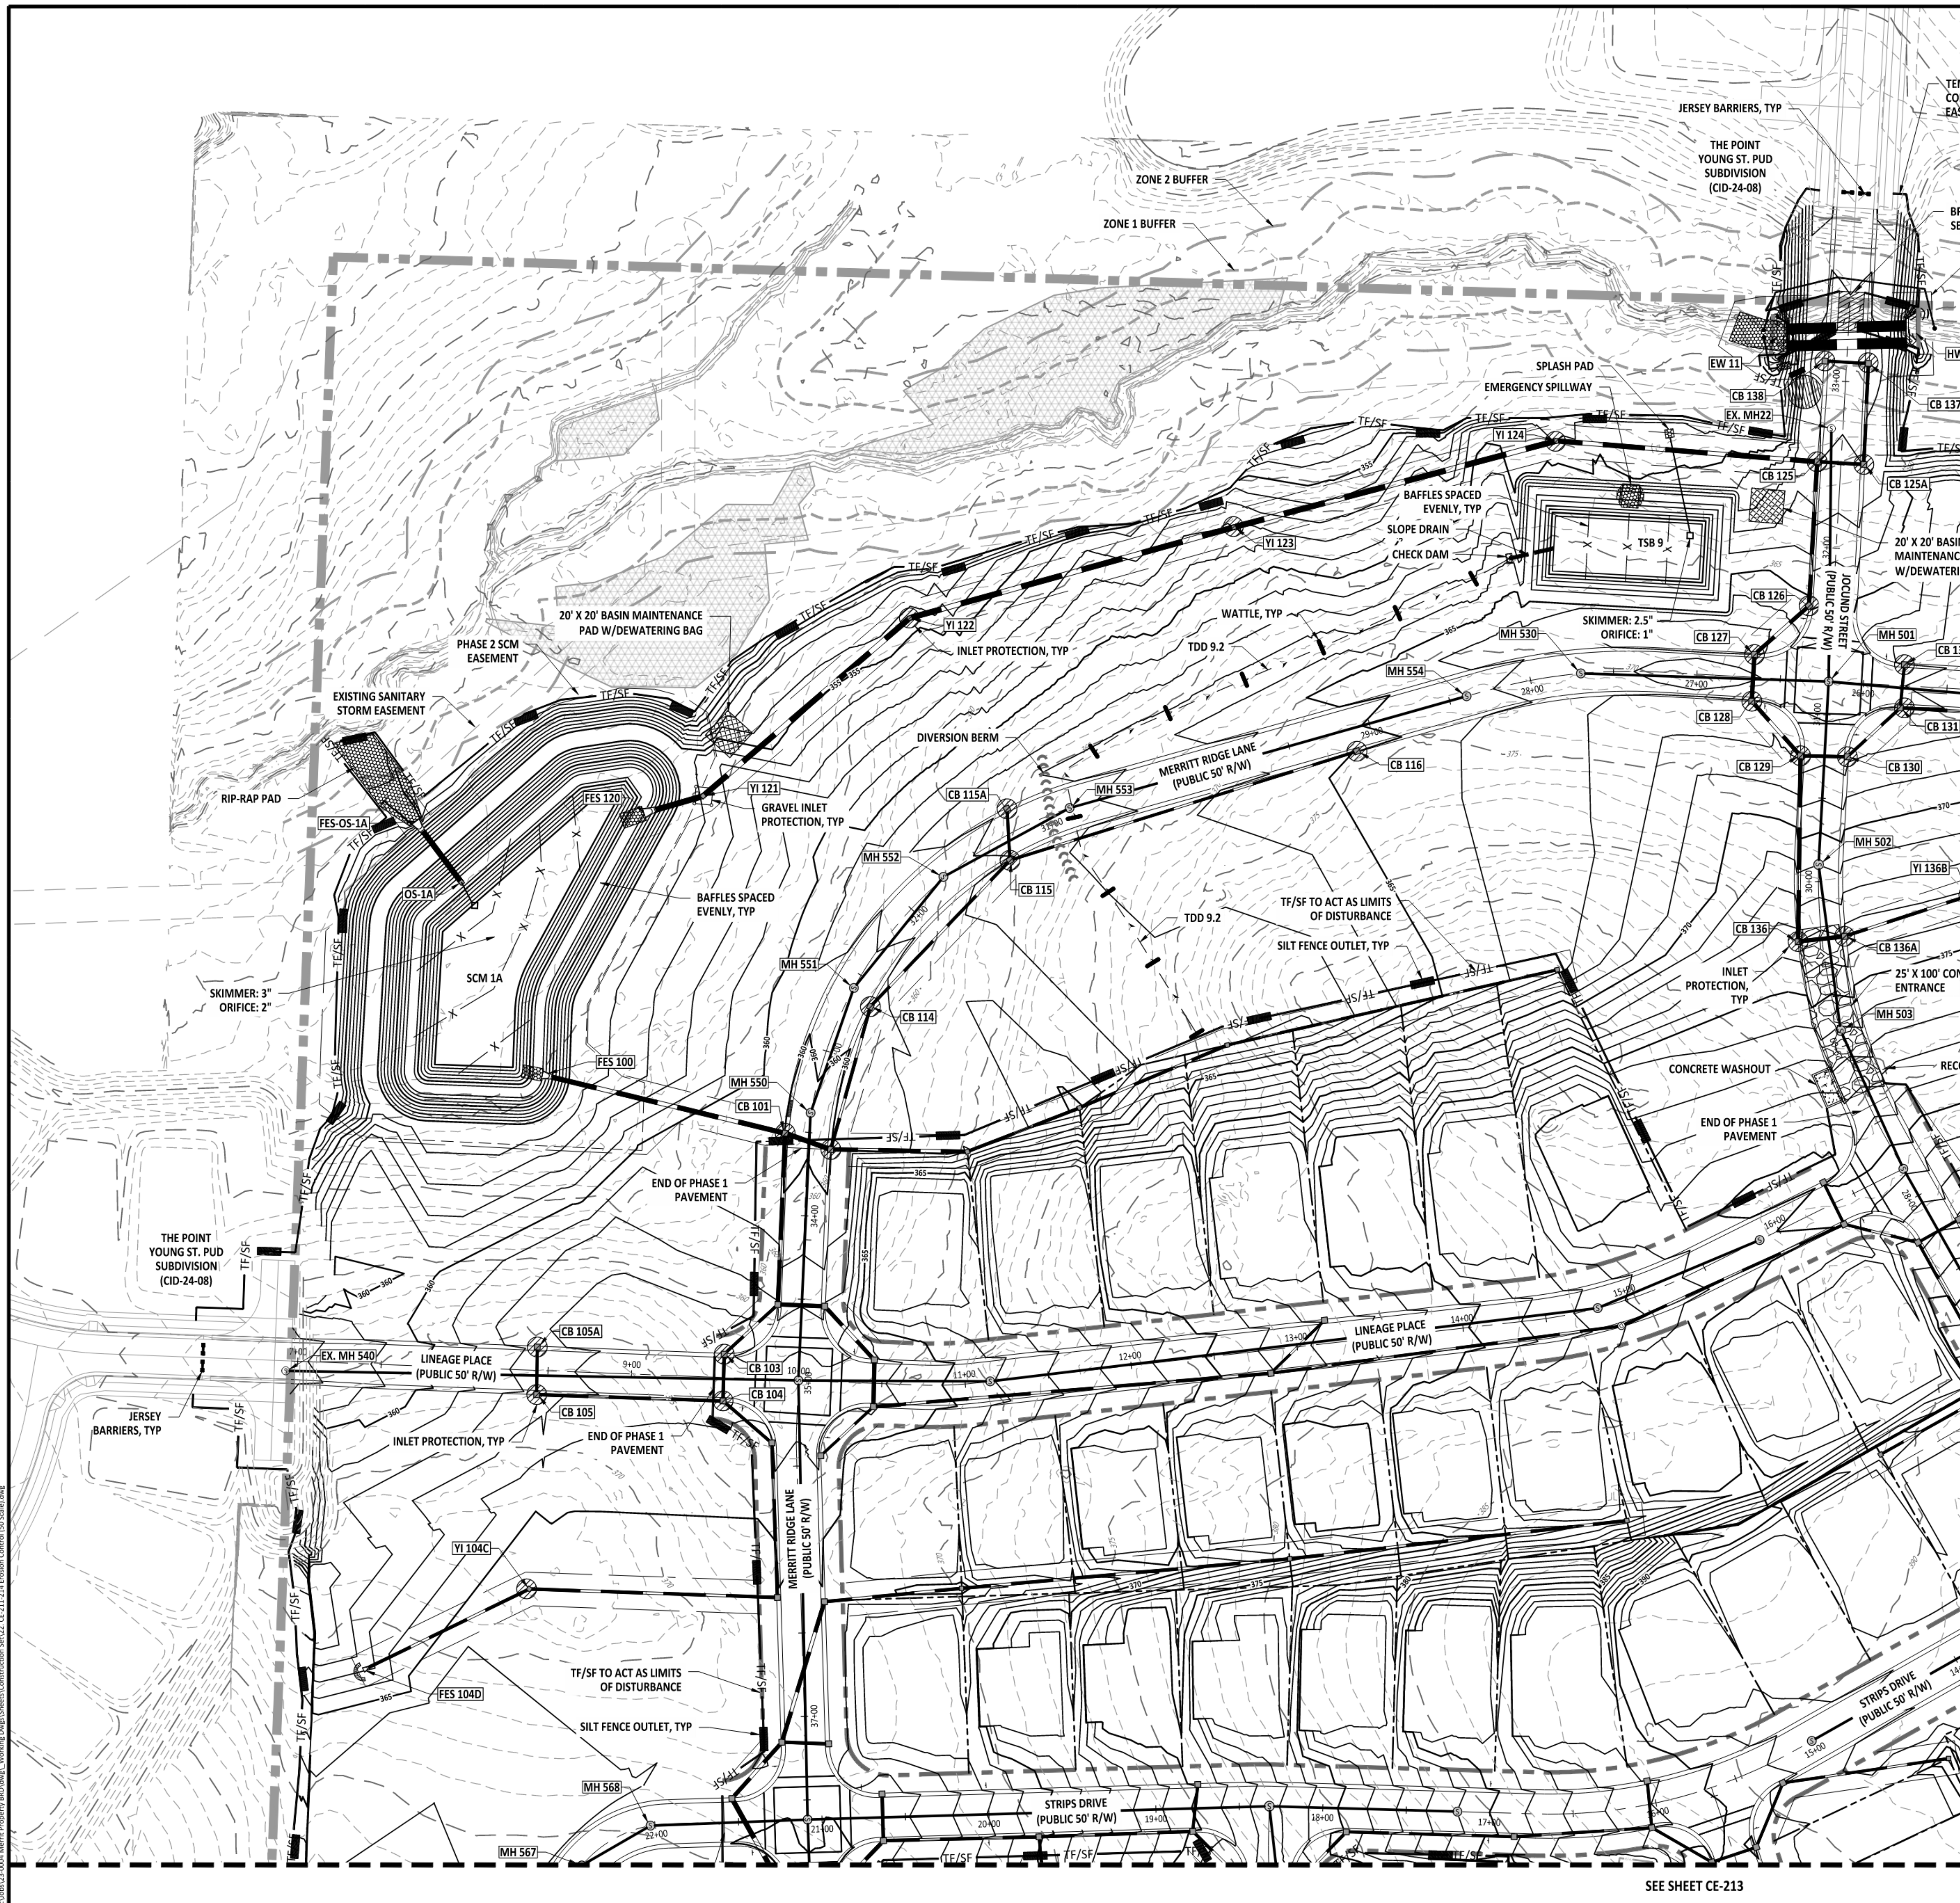


EROSION CONTROL LEGEND		REFERENCE DETAIL
	SILT FENCE/TREE PROTECTION FENCE COMBO (LOD)	01 / CE501
	LIMITS OF DISTURBANCE	SEE PLANS
	TREE PROTECTION FENCE (LOD)	08 / CE502
	TEMPORARY DIVERSION DITCH	06 / CE500 & CE504
	BAFFLE	05 / CE501
	SILT FENCE OUTLET	02 / CE501
	SEDIMENT SACK INLET PROTECTION	03 / CE501
	STANDARD PIPE INLET PROTECTION	08 / CE501
	GRAVEL INLET PROTECTION	04 / CE500
	GRAVEL CHECK DAM	03 / CE500
	MAINTENANCE PAD	06 / CE502
	RIPRAP DISSIPATOR	07 & 08 / CE500
	SLOPE DRAIN/DRAINAGE PIPE	09 / CE500
	WATTLE	05 / CE500
	SKIMMER	01 / CE502
	TEMPORARY SKIMMER BASIN	05 & 06 / CE501
	STAGING AND LAYDOWN AREA	NGC01 / CE503
	CONSTRUCTION ENTRANCE	02 / CE500
	CONCRETE WASHOUT PIT	NGC01 / CE503
	BRIDGE MAT	03 / CE502
	FUTURE PHASE 2 & 3	N/A


SITE LEGEND	
	PROPERTY BOUNDARY
	NEUSE RIVER BUFFER ZONE 1
	NEUSE RIVER BUFFER ZONE 2
	LIMITS OF DISTURBANCE
	WETLANDS

GENERAL NOTES:

1. ROLLED EROSION CONTROL PRODUCT (RECP) SHALL BE INSTALLED WHERE THE DIFFERENCE IN ELEVATION IS GREATER THAN 10 FT, WITHIN BASINS, AND WHERE SLOPES ARE GREATER THAN 3:1.
2. SEE SHEET G-005 FOR TEMPORARY DIVERSION DITCH (TDD) AND SLOPE DRAIN SIZING SCHEDULE.

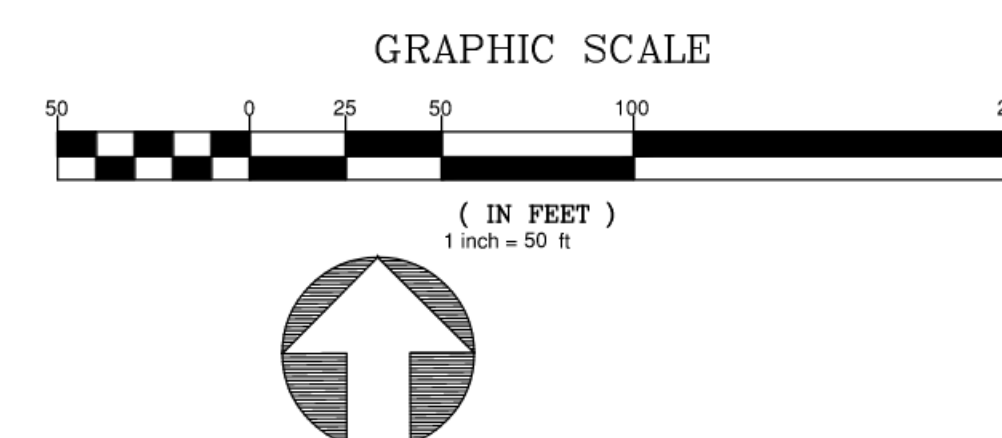

North Carolina 811
*** 3 Days Before Digging ***
North Carolina 811
811 or 1-800-632-4949
Remote Ticket Entry
<http://nc811.org/remoteticketentry.htm>

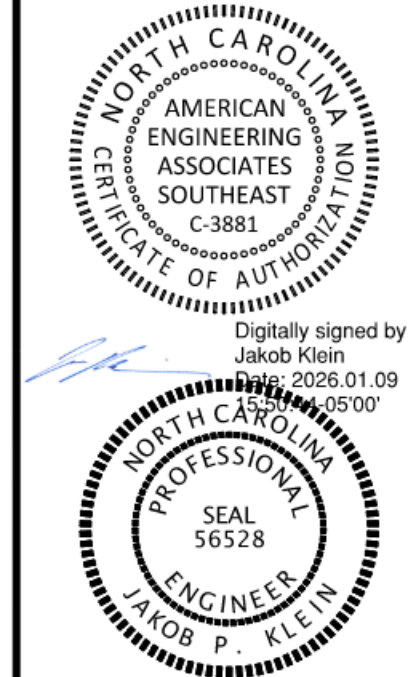[illegible]

STIPULATION FOR REUSE


THIS DRAWING WAS PREPARED FOR USE ON THE SPECIFIC SITE, NAMED HEREON, CONTEMPORANEOUSLY WITH ITS ISSUE DATE AS LISTED, HEREON, AND IT IS NOT SUITABLE FOR USE ON A DIFFERENT PROJECT SITE OR AT A LATER TIME. USE OF THIS DRAWING FOR REFERENCE OR EXAMPLE ON ANOTHER PROJECT REQUIRES THE SERVICES OF PROPERLY LICENSED ARCHITECTS AND ENGINEERS. REPRODUCTION OF THIS DRAWING FOR REUSE ON ANOTHER PROJECT IS NOT AUTHORIZED, AND MAY BE CONTRARY TO THE LAW.

MERRITT RESERVE VE
 EROSION CONTROL
 PHASE 2 & 3 STAGE 2
 ROLESVILLE RD
 WAKE COUNTY NC 27312


JOB NUMBER:	23-000
CHECKED BY:	J
DRAWN BY:	DH/MA/L
DATE:	12/12/202
SHEET TITLE:	

**EROSION
CONTROL PHASE
2 & 3 STAGE 2**

SHEET NO.: **CE-212**





Z:\delv12.0008 Merritt Property (BUD)dwg\Working Draw\Sheets\Construction\Set\217_CE-217-218 Erosion Control (D) Scaled.dwg
2025-12-12

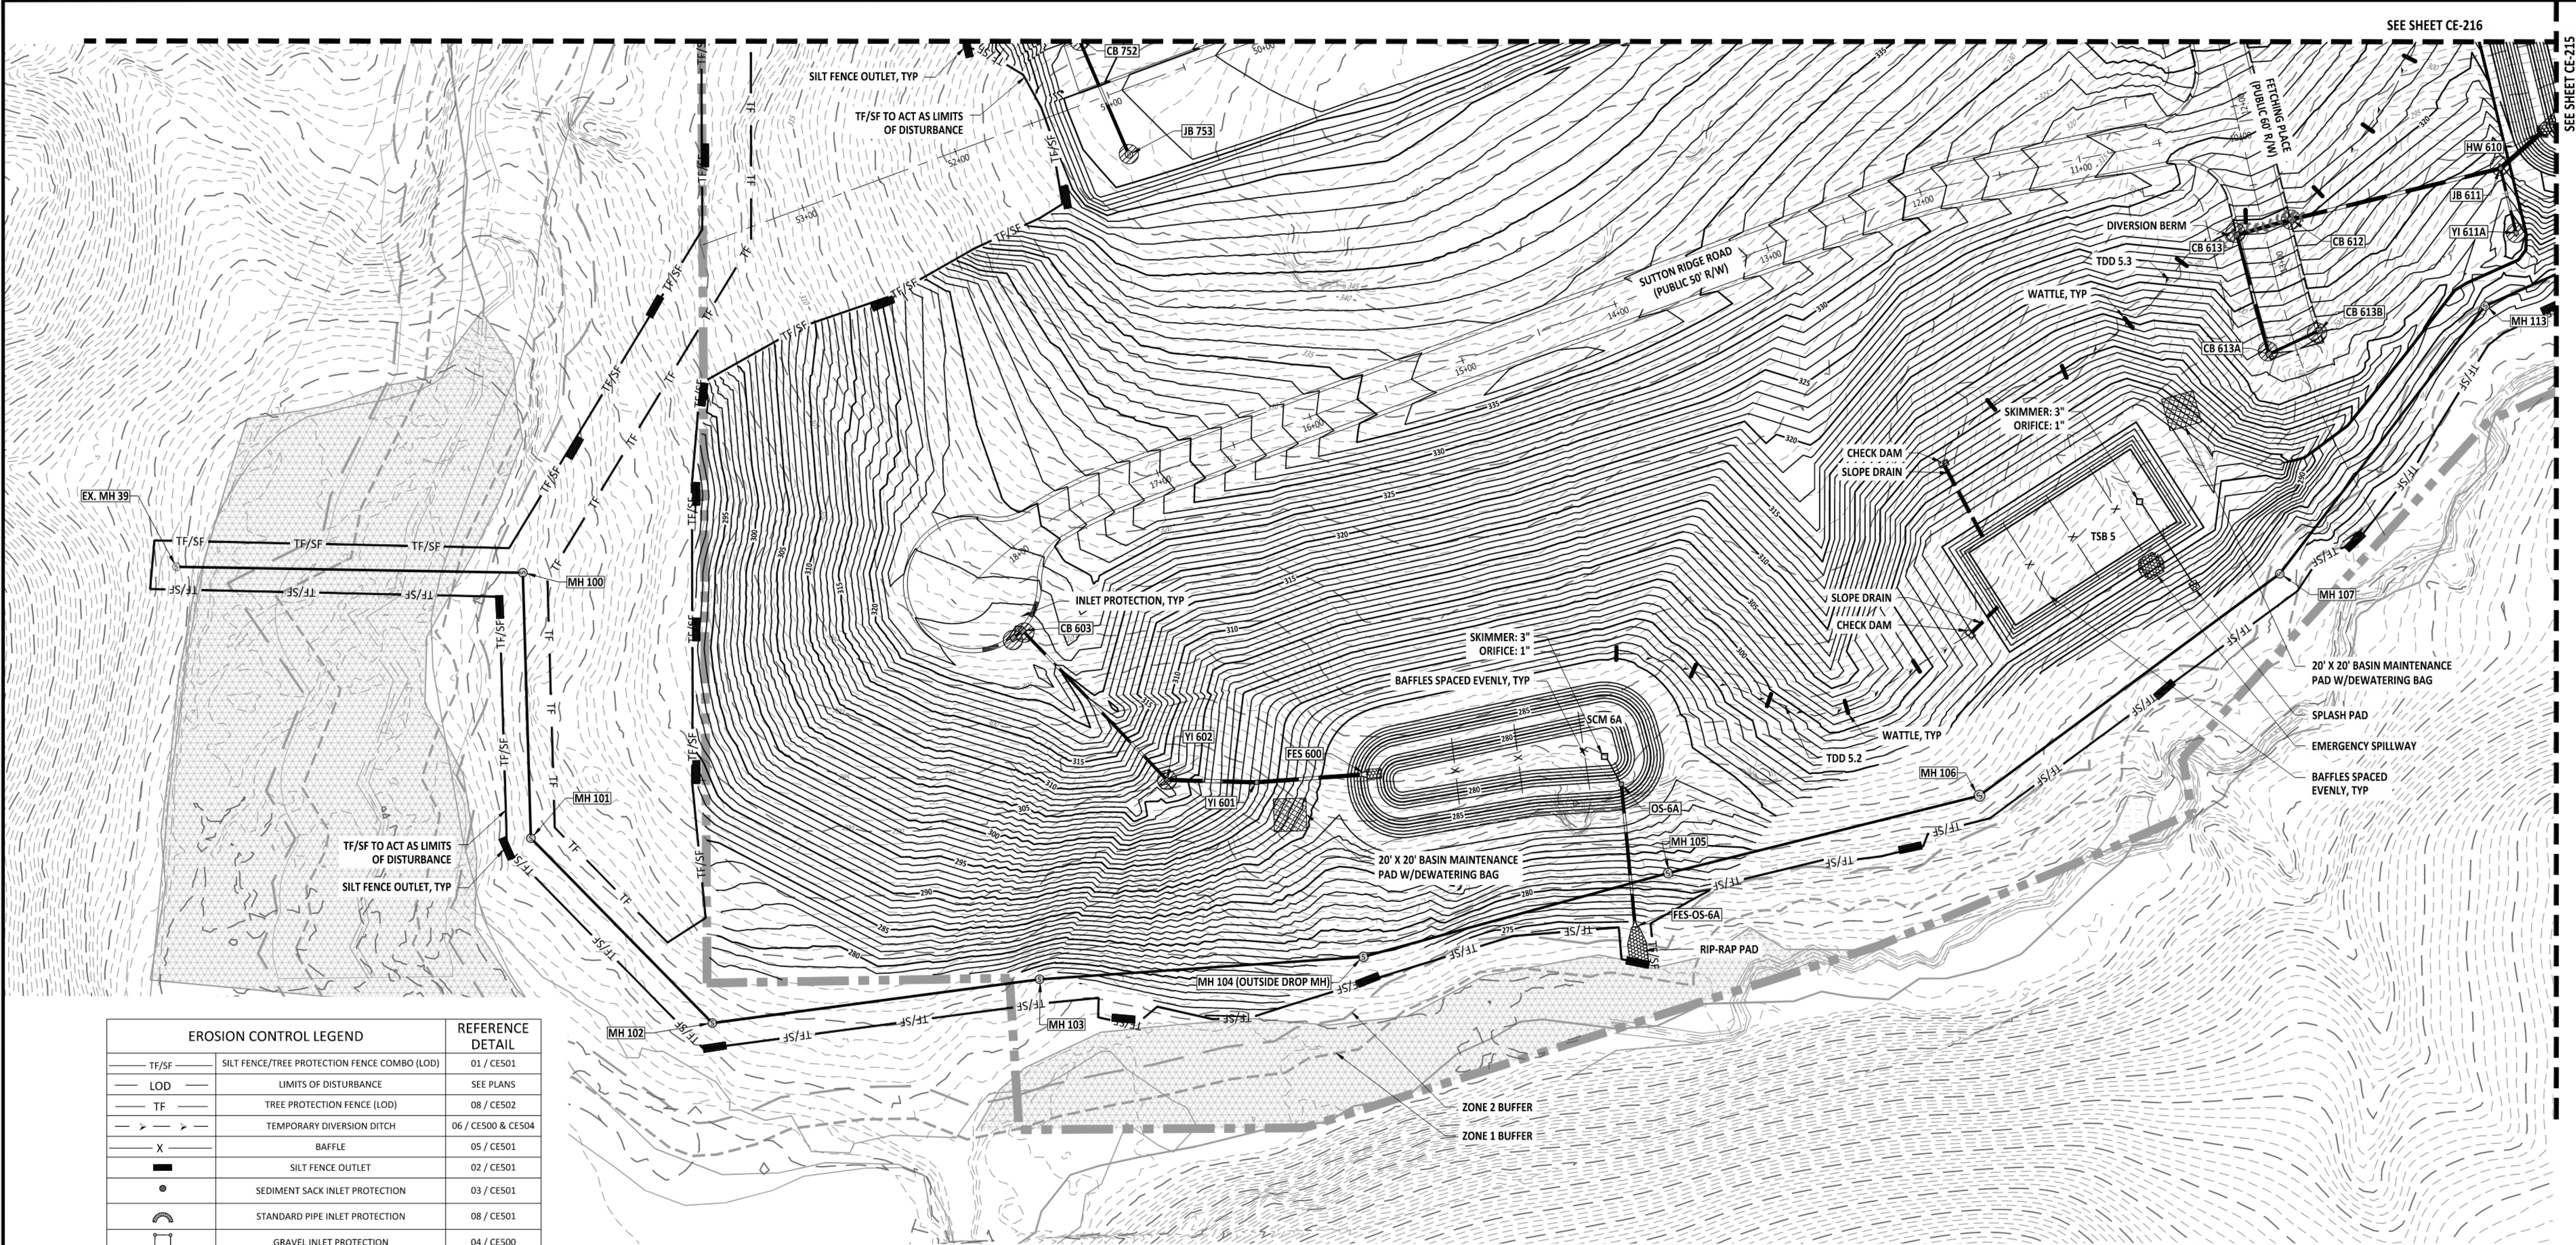

EROSION CONTROL LEGEND		REFERENCE DETAIL
TF/SF	SILT FENCE/TREE PROTECTION FENCE COMBO (LOD)	01 / CE501
LOD	LIMITS OF DISTURBANCE	SEE PLANS
TF	TREE PROTECTION FENCE (LOD)	08 / CE502
--->---	TEMPORARY DIVERSION DITCH	06 / CE500 & CE504
X	BAFFLE	05 / CE501
●	SILT FENCE OUTLET	02 / CE501
○	SEDIMENT SACK INLET PROTECTION	03 / CE501
⌣	STANDARD PIPE INLET PROTECTION	08 / CE501
□	GRAVEL INLET PROTECTION	04 / CE500
▣	GRAVEL CHECK DAM	03 / CE500
▤	MAINTENANCE PAD	06 / CE502
▥	RIPRAP DISSIPATOR	07 & 08 / CE500
▧	SLOPE DRAIN/DRAINAGE PIPE	09 / CE500
▨	WATTLE	05 / CE500
▩	SKIMMER	01 / CE502
▪	TEMPORARY SKIMMER BASIN	05 & 06 / CE501
▫	STAGING AND LAYDOWN AREA	NCG01 / CE503
▬	CONSTRUCTION ENTRANCE	02 / CE500
▮	CONCRETE WASHOUT PIT	NCG01 / CE503
▯	BRIDGE MAT	03 / CE502
▰	FUTURE PHASE 2 & 3	N/A


SITE LEGEND	
---	PROPERTY BOUNDARY
---	NEUSE RIVER BUFFER ZONE 1
---	NEUSE RIVER BUFFER ZONE 2
---	LIMITS OF DISTURBANCE
▨	WETLANDS

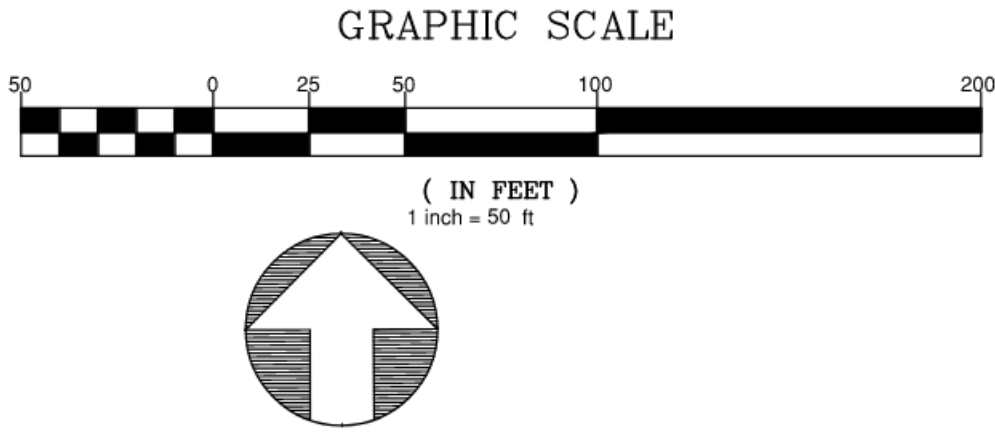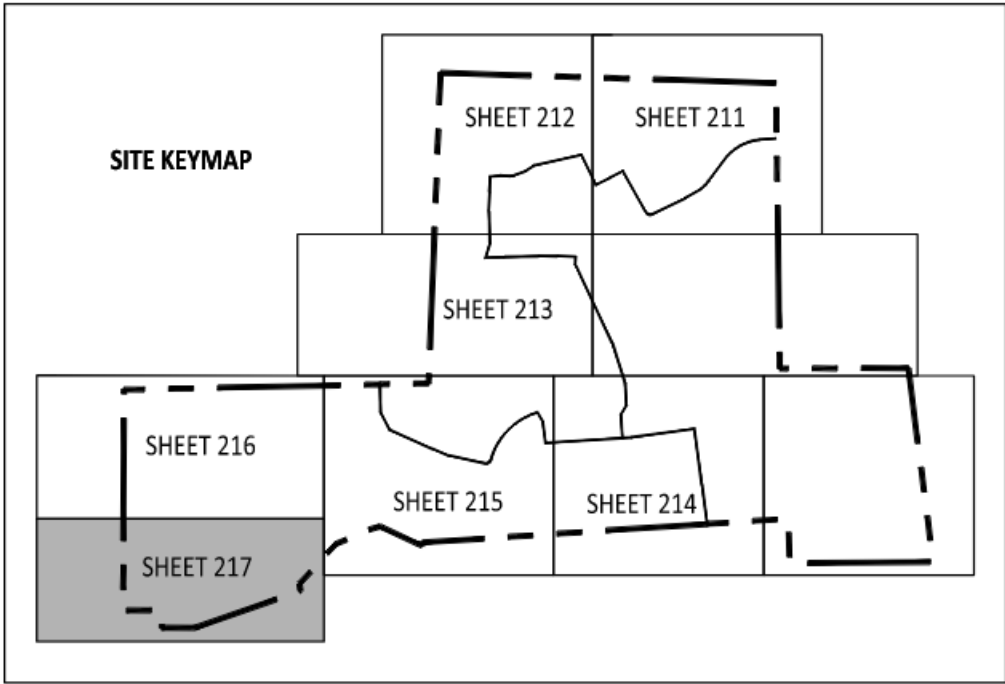

- GENERAL NOTES:
- ROLLED EROSION CONTROL PRODUCT (RECP) SHALL BE INSTALLED WHERE THE DIFFERENCE IN ELEVATION IS GREATER THAN 10 FT, WITHIN BASINS, AND WHERE SLOPES ARE GREATER THAN 3:1.
 - SEE SHEET G-005 FOR TEMPORARY DIVERSION DITCH (TDD) AND SLOPE DRAIN SIZING SCHEDULE.



PROJECT NUMBER = CID-25-02

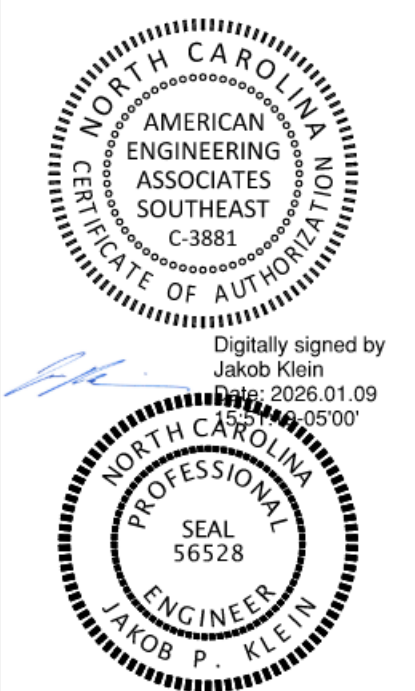

NO.	DATE	REVISION:

STIPULATION FOR REUSE

THIS DRAWING WAS PREPARED FOR USE ON THE SPECIFIC SITE, NAMED HEREON, CONTEMPORANEOUSLY WITH ITS ISSUE DATE AS LISTED, HEREON, AND IT IS NOT SUITABLE FOR USE ON A DIFFERENT PROJECT SITE OR AT A LATER TIME. USE OF THIS DRAWING FOR REFERENCE OR EXAMPLE ON ANOTHER PROJECT REQUIRES THE SERVICES OF PROPERLY LICENSED ARCHITECTS AND ENGINEERS. REPRODUCTION OF THIS DRAWING FOR REUSE ON ANOTHER PROJECT IS NOT AUTHORIZED AND MAY BE CONTRARY TO THE LAW.



MERRITT RESERVE
EROSION CONTROL
PHASE 2 & 3 STAGE 2
ROLESVILLE RD
WAKE COUNTY NC 27312

JOB NUMBER:	23-0004
CHECKED BY:	JK
DRAWN BY:	DH/MA/LL
DATE:	12/12/2025

SHEET TITLE:
EROSION CONTROL PHASE 2 & 3 STAGE 2

SHEET NO.:
CE-217

SITE LEGEND	
	PROPERTY BOUNDARY
	NEUSE RIVER BUFFER ZONE 1
	NEUSE RIVER BUFFER ZONE 2
	LIMITS OF DISTURBANCE
	WETLANDS

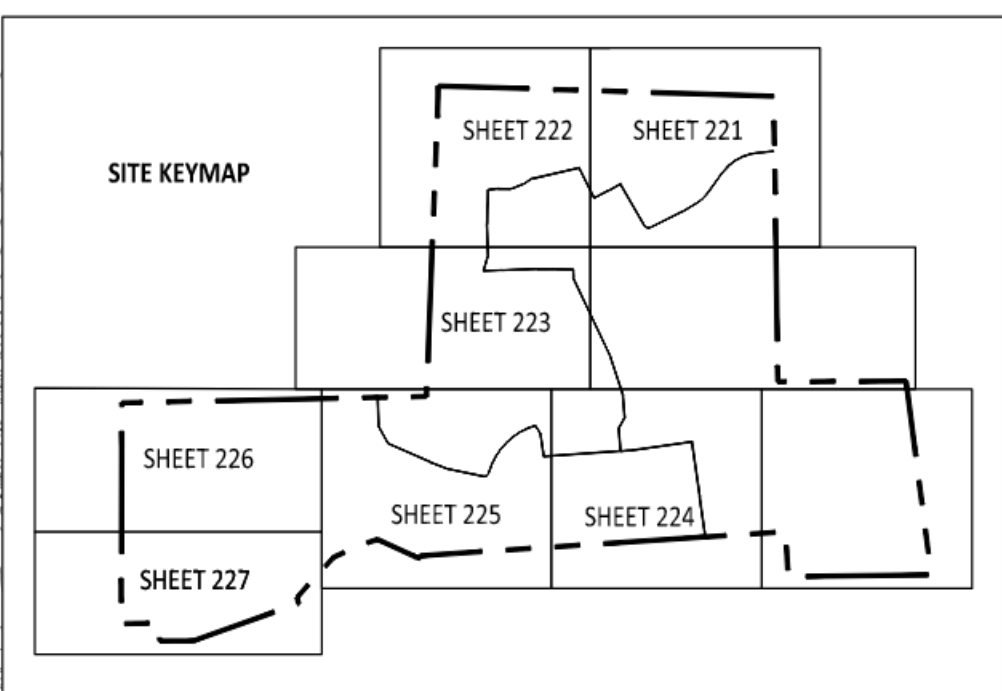

**AMERICAN
Engineering**
American Engineering Associates - Southeast, P.A.
4020 Westchase Boulevard, Suite 450
Raleigh, NC 27607
919-469-1101



Digitally signed by
Jakob Klein
Date: 2026.01.09
15:56:06 +05'00'

[illegible]

STIPULATION FOR REUSE

THIS DRAWING WAS PREPARED FOR USE ON THE SPECIFIC SITE, NAMED HEREON, CONTEMPORANEOUSLY WITH ITS ISSUE DATE AS LISTED, HEREON. AND IT IS NOT SUITABLE FOR USE ON A DIFFERENT PROJECT SITE OR AT A LATER TIME. USE OF THIS DRAWING FOR REFERENCE OR EXAMINATION ON ANOTHER PROJECT REQUIRES THE SERVICES OF PROPERLY LICENSED ARCHITECTS AND ENGINEERS. REPRODUCTION OF THIS DRAWING FOR REUSE ON ANOTHER PROJECT IS NOT AUTHORIZED AND MAY BE CONTRARY TO THE LAW.

MERRITT RESERVE
EROSION CONTROL PHASE 2 & 3
STAGE 3 OVERALL
ROLESVILLE RD
WAKE COUNTY NC 27312


JOB NUMBER:	23-0004
CHECKED BY:	JK
DRAWN BY:	DH/MA/LL
DATE:	12/12/2025









SHEET TITLE:
**EROSION
CONTROL PHASE
2 & 3 STAGE 3
OVERALL**

SHEET NO.:
CE-220



SHEET NO.: **CE-222**

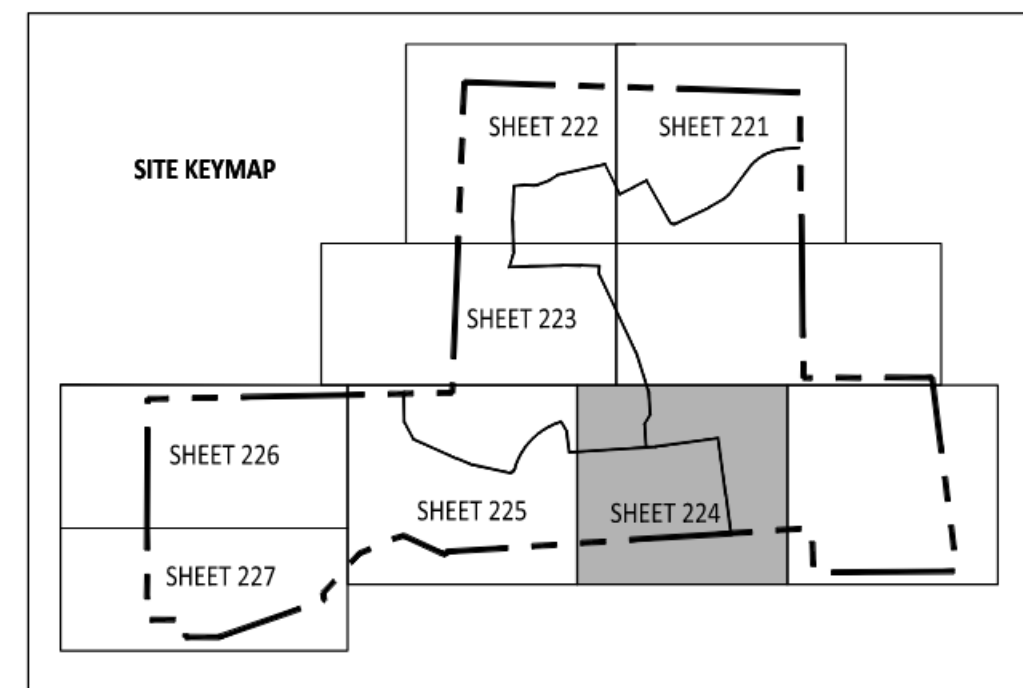


EROSION CONTROL LEGEND		REFERENCE DETAIL
	SILT FENCE/TREE PROTECTION FENCE COMBO (LOD)	01 / CE501
	LIMITS OF DISTURBANCE	SEE PLANS
	TREE PROTECTION FENCE (LOD)	08 / CE502
	TEMPORARY DIVERSION DITCH	06 / CE500 & CE504
	BAFFLE	05 / CE501
	SILT FENCE OUTLET	02 / CE501
	SEDIMENT SACK INLET PROTECTION	03 / CE501
	STANDARD PIPE INLET PROTECTION	08 / CE501
	GRAVEL INLET PROTECTION	04 / CE500
	GRAVEL CHECK DAM	03 / CE500
	MAINTENANCE PAD	06 / CE502
	RIPRAP DISSIPATOR	07 & 08 / CE500
	SLOPE DRAIN/DRAINAGE PIPE	09 / CE500
	WATTLE	05 / CE500
	SKIMMER	01 / CE502
	TEMPORARY SKIMMER BASIN	05 & 06 / CE501
	STAGING AND LAYDOWN AREA	NGC01 / CE503
	CONSTRUCTION ENTRANCE	02 / CE500
	CONCRETE WASHOUT PIT	NGC01 / CE503
	BRIDGE MAT	03 / CE502
	FUTURE PHASE 2 & 3	N/A



SITE LEGEND	
	PROPERTY BOUNDARY
	NEUSE RIVER BUFFER ZONE 1
	NEUSE RIVER BUFFER ZONE 2
	LIMITS OF DISTURBANCE
	WETLANDS

GENERAL NOTES:



- 1. ROLLED EROSION CONTROL PRODUCT (RECP) SHALL BE INSTALLED WHERE THE DIFFERENCE IN ELEVATION IS GREATER THAN 10 FT, WITHIN BASINS, AND WHERE SLOPES ARE GREATER THAN 3:1.**

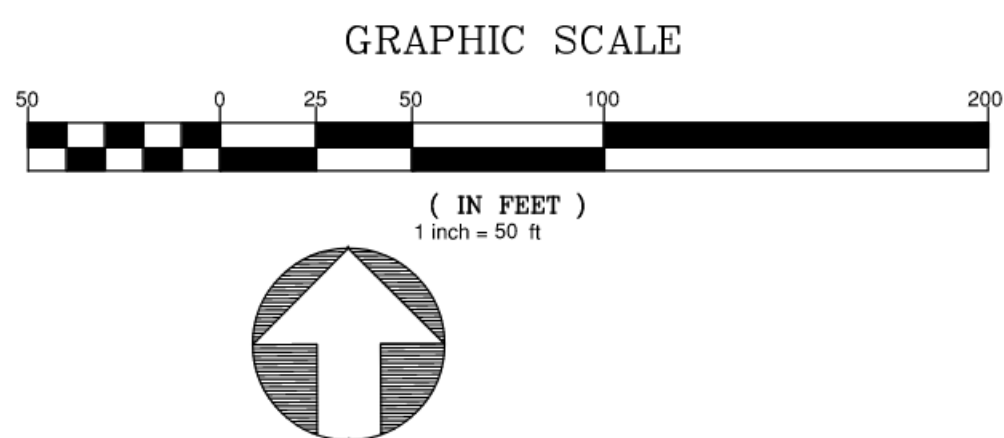

North Carolina 811
 *** 3 Days Before Digging ***
 North Carolina 811
 811 or 1-800-632-4949
 Remote Ticket Entry
<http://nc811.org/remoteticketentry.htm>



1. UPON COMPLETION OF PIPE INSTALLATION, REMOVE TEMPORARY SANDBAGS ON DOWNSTREAM END.
2. REMOVE TEMPORARY SANDBAGS ON UPSTREAM END.
3. INSTALL SILT FENCE AT THE TOE OF SLOPES AND TIE TO ENDWALLS AS SHOWN ON THIS PLAN.
4. COMPLETE FILL AROUND THE PIPE TO A LEVEL AT LEAST TWO (2) FEET ABOVE THE TOP OF THE PIPE TO ALLOW CONSTRUCTION EQUIPMENT TO PASS OVER IT.
5. COMPLETE FILL BRINGING THE AREA TO FINISHED GRADE.
6. INSTALL PAVEMENT AND FOLLOW THE SEEDING SCHEDULE FOR ALL BARE AREAS.
7. REFER TO MAIN CONSTRUCTION SEQUENCE FOR OTHER DETAILS.



Digitally signed by
Jakob Klein
Date: 2026.01.09

[illegible]

STIPULATION FOR REUSE

THIS DRAWING WAS PREPARED FOR USE ON THE SPECIFIC SITE, NAMED HEREON. CONTEMPORANEOUSLY WITH ITS ISSUE DATE AS LISTED, HEREON, AND IT IS NOT SUITABLE FOR USE ON A DIFFERENT PROJECT SITE OR AT A LATER TIME. USE OF THIS DRAWING FOR REFERENCE OR EXAMPLE ON ANOTHER PROJECT REQUIRES THE SERVICES OF PROPERLY LICENSED ARCHITECTS AND ENGINEERS. REPRODUCTION OF THIS DRAWING FOR REUSE ON ANOTHER PROJECT IS NOT AUTHORIZED AND MAY BE CONTRARY TO THE LAW.




MERRITT RESERVE
EROSION CONTROL CULVERT
CROSSING PHASE 2 & 3
ROLESVILLE RD
WAKE COUNTY NC 27312

LAB NUMBER:	23-0004
CHECKED BY:	JK
DRAWN BY:	DH/MA/LL
DATE:	12/12/2025

**EROSION CONTROL
CULVERT CROSSING
PHASE 2 & 3**

SHEET NO.: **CE-240**

SITE LEGEND	
	PROPERTY BOUNDARY
	NEUSE RIVER BUFFER ZONE 1
	NEUSE RIVER BUFFER ZONE 2
	LIMITS OF DISTURBANCE
	WETLANDS

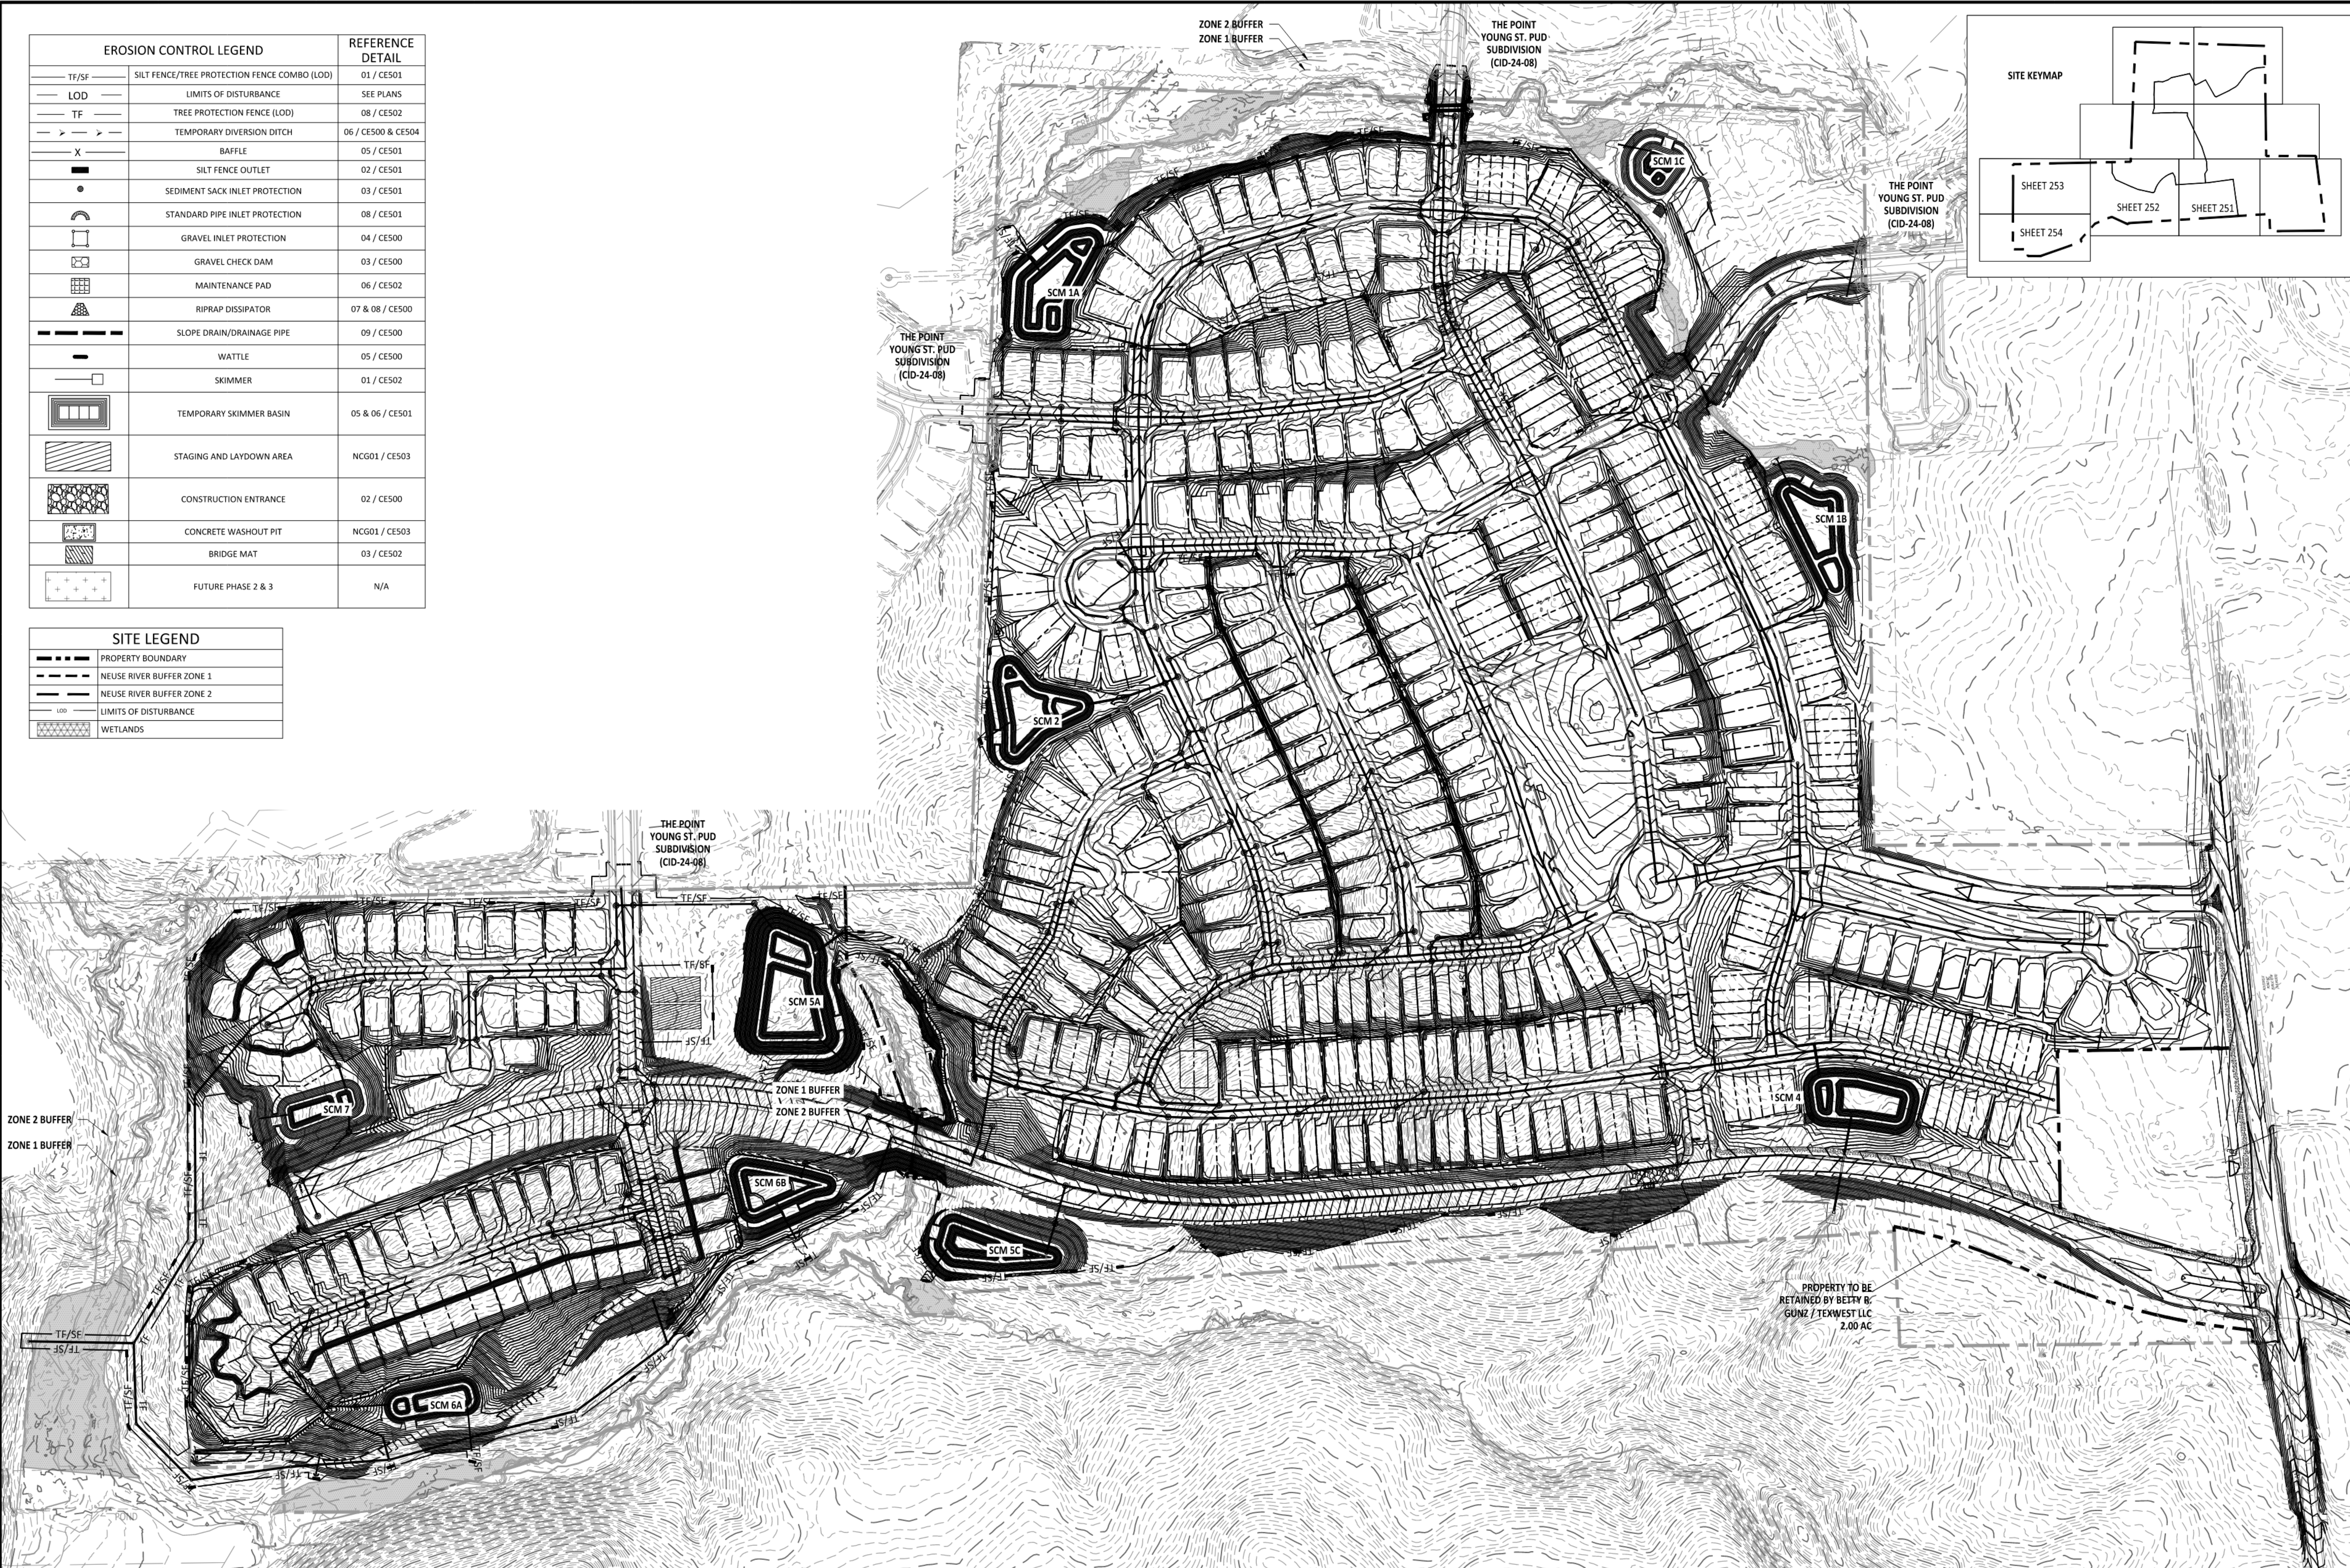

North Carolina
*** 3 Days Before Digging ***
North Carolina 811
811 or 1-800-632-4949
Remote Ticket Entry
<http://nc811.org/remoteticketentry.htm>

PROJECT NUMBER = CID-25-02

AMERICAN
Engineering

American Engineering Associates - Southeast, P.A.
4020 Westchase Boulevard, Suite 450
Raleigh, NC 27607
919-469-1101



Digitally signed by
Jakob Klein
Date: 2026.01.09

[illegible]

STIPULATION FOR REUSE


THIS DRAWING WAS PREPARED FOR USE ON THE SPECIFIC SITE, NAMED HEREON, CONTEMPORANEOUSLY WITH ITS ISSUE DATE AS LISTED, HEREON, AND IT IS NOT SUITABLE FOR USE ON A DIFFERENT PROJECT SITE OR AT A LATER TIME. USE OF THIS DRAWING FOR REFERENCE OR EXAMPLE ON ANOTHER PROJECT REQUIRES THE SERVICES OF PROPERLY LICENSED ARCHITECTS AND ENGINEERS. REPRODUCTION OF THIS DRAWING FOR REUSE ON ANOTHER PROJECT IS NOT AUTHORIZED AND MAY BE CONTRARY TO THE LAW.

MERRITT RESERVE
EROSION CONTROL PHASE 3
STAGE 1 OVERALL
ROLESVILLE RD
WAKE COUNTY NC 27312

JOB NUMBER:	23-0004
CHECKED BY:	JL
DRAWN BY:	DH/MA/L
DATE:	12/12/2023

SHEET TITLE:
**EROSION
CONTROL PHASE
3 STAGE 1
OVERALL**


SHEET NO.: **CE-250**

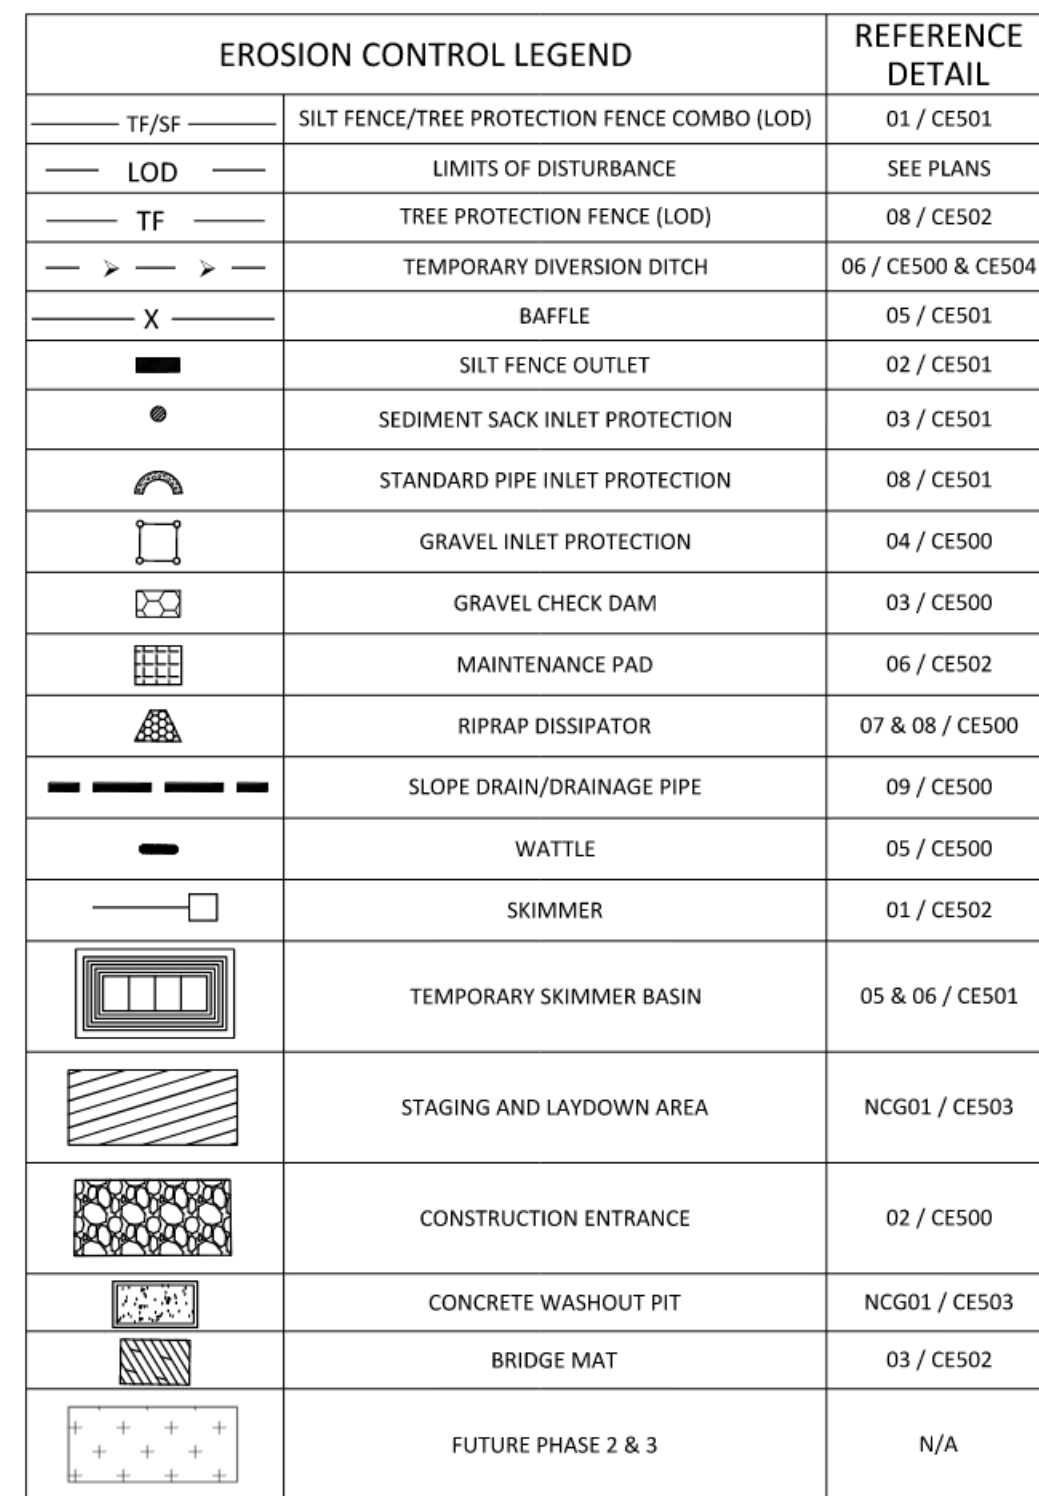

SITE LEGEND	
	PROPERTY BOUNDARY
	NEUSE RIVER BUFFER ZONE 1
	NEUSE RIVER BUFFER ZONE 2
	LIMITS OF DISTURBANCE
	WETLANDS

GENERAL NOTES:

1. ROLLED EROSION CONTROL PRODUCT (RECP) SHALL BE INSTALLED WHERE THE DIFFERENCE IN ELEVATION IS GREATER THAN 10 FT, WITHIN BASINS, AND WHERE SLOPES ARE GREATER THAN 3:1.

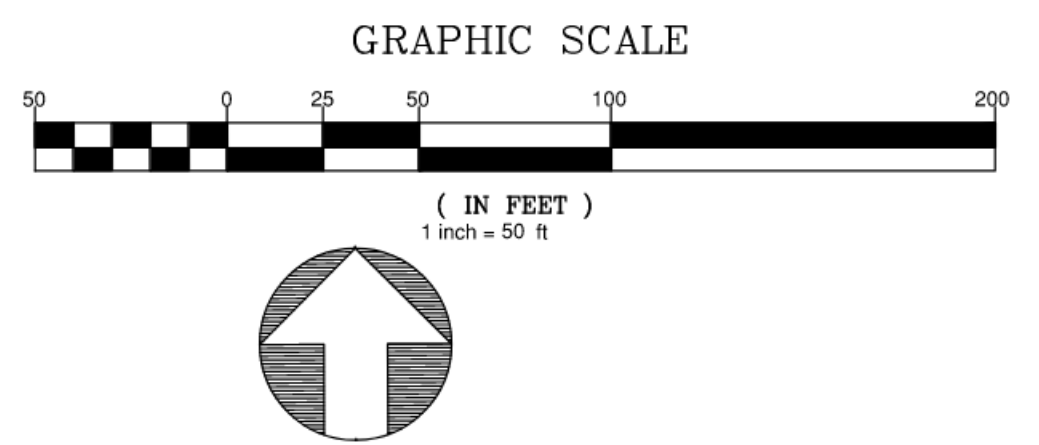


North Carolina 811
*** 3 Days Before Digging ***
North Carolina 811
811 or 1-800-632-4949
Remote Ticket Entry
<http://nc811.org/remoteticketentry.htm>

PROJECT NUMBER = CID-25-02





Z:\N01012-0004 Merritt Property (BID)\Drawings\Working Drawings\Construction Set\2506, CE-252, 253, 254 Erosion Control (3D) Sheet.dwg
2/26/2025 12:12

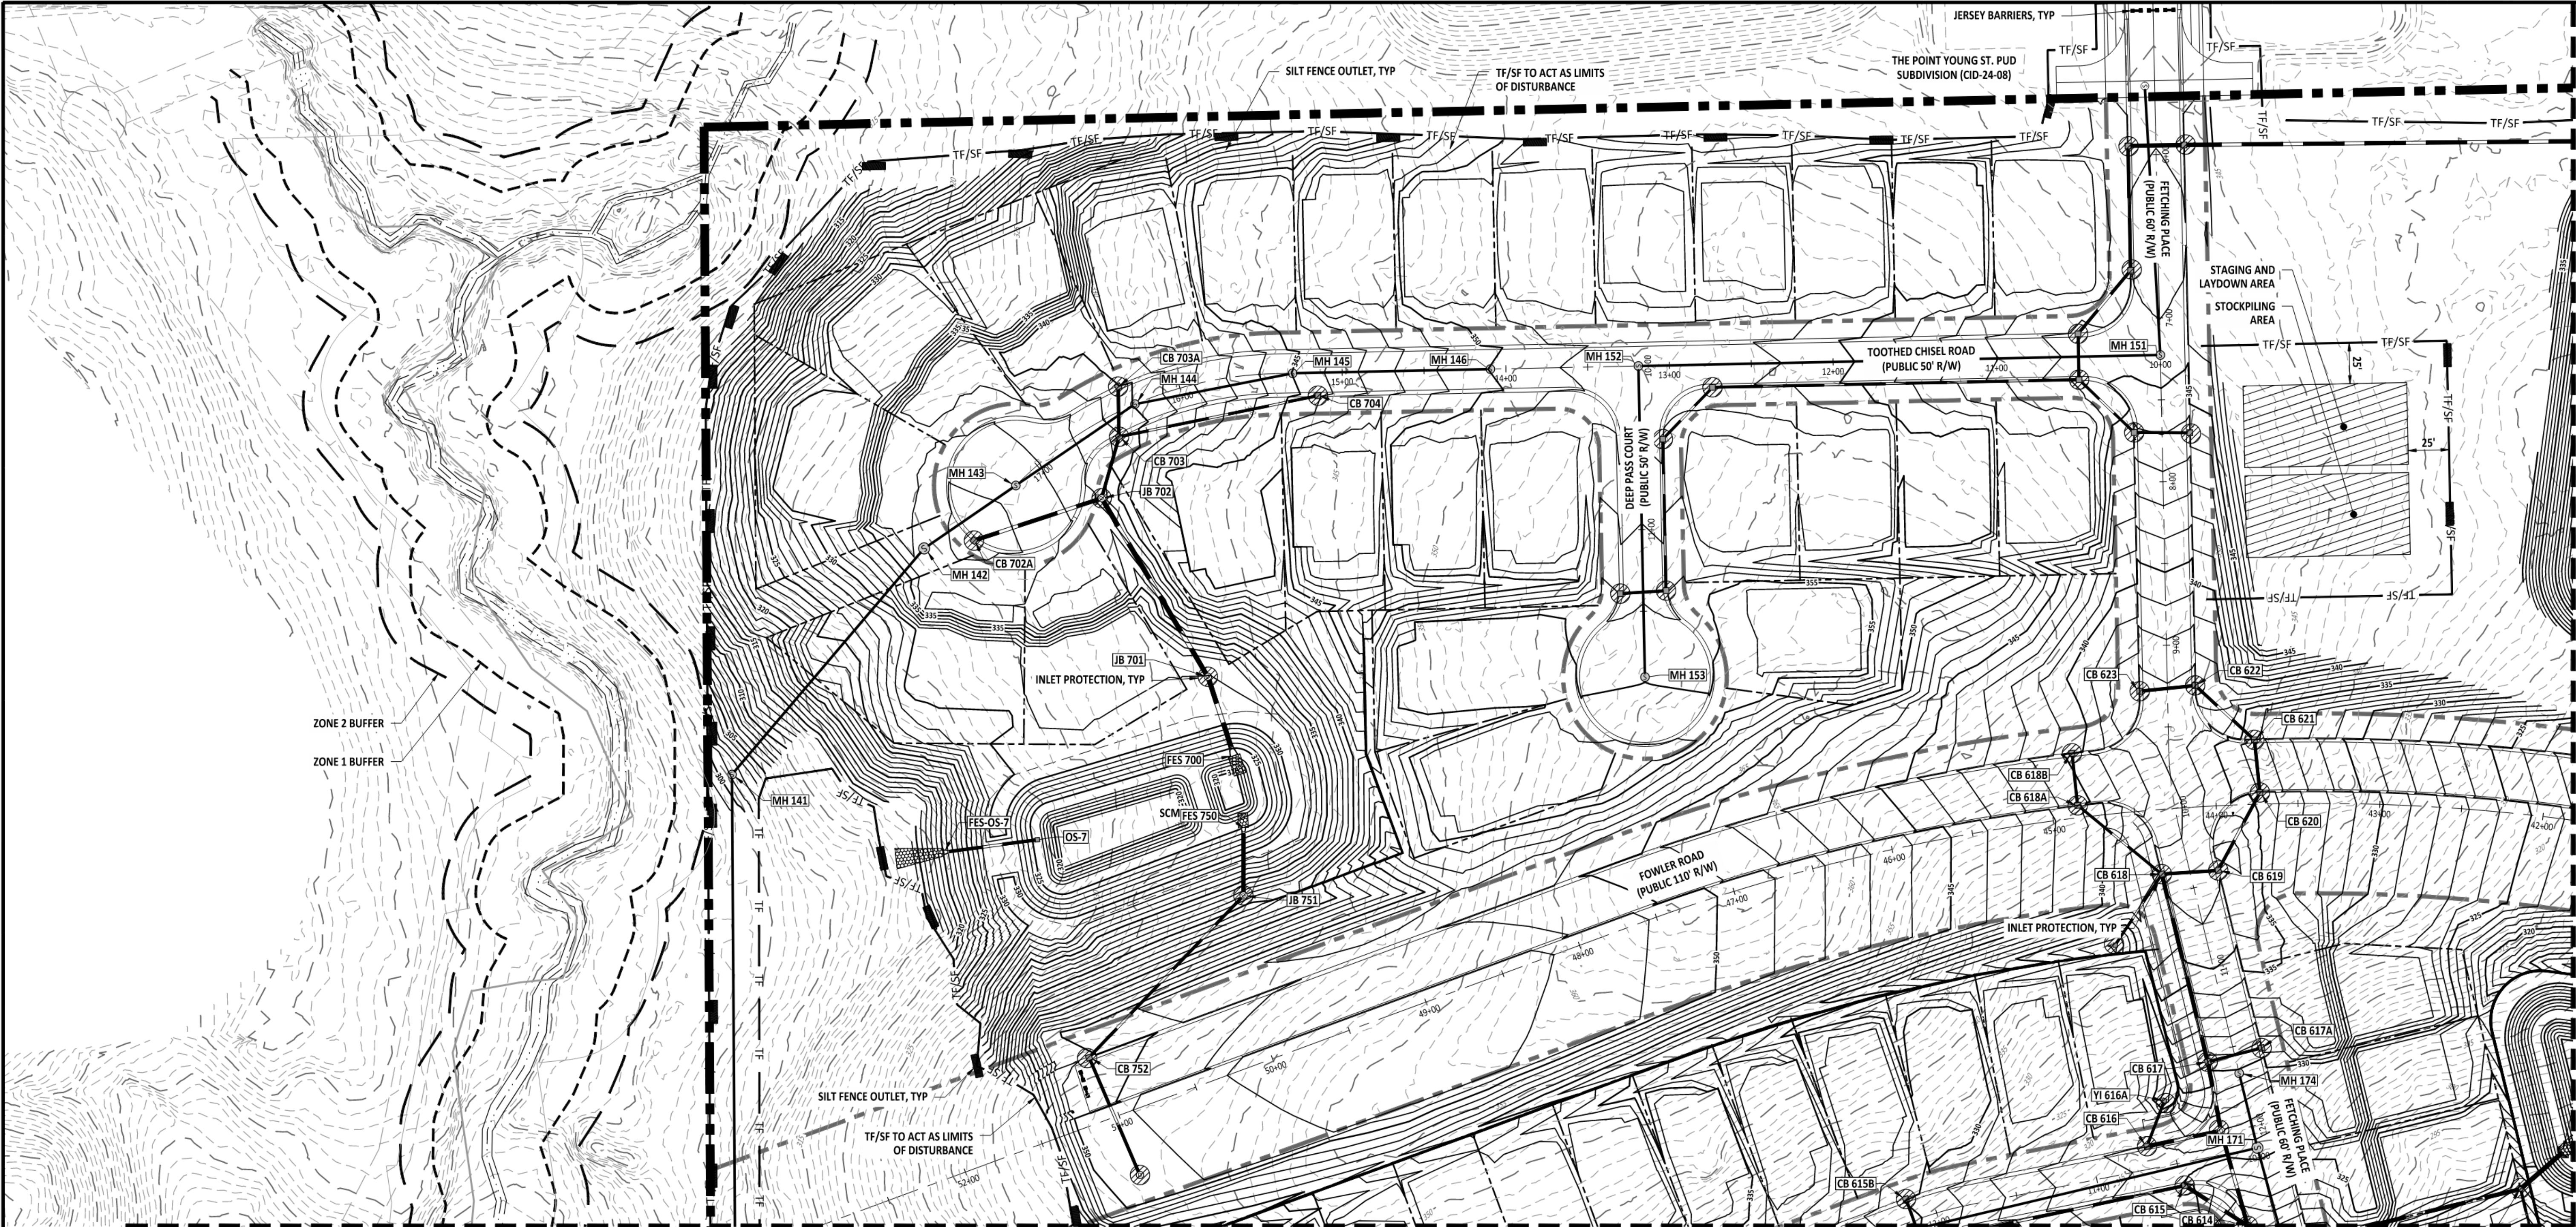

EROSION CONTROL LEGEND		REFERENCE DETAIL
TF/SF	SILT FENCE/TREE PROTECTION FENCE COMBO (LOD)	01 / CE501
LOD	LIMITS OF DISTURBANCE	SEE PLANS
TF	TREE PROTECTION FENCE (LOD)	08 / CE502
	SILT FENCE OUTLET	02 / CE501
	SEDIMENT SACK INLET PROTECTION	03 / CE501
	STANDARD PIPE INLET PROTECTION	08 / CE501
	GRAVEL INLET PROTECTION	04 / CE500
	GRAVEL CHECK DAM	03 / CE500
	MAINTENANCE PAD	06 / CE502
	RIPRAP DISSIPATOR	07 & 08 / CE500
	SLOPE DRAIN/DRAINAGE PIPE	09 / CE500
	STAGING AND LAYDOWN AREA	NCG01 / CE503
	CONSTRUCTION ENTRANCE	02 / CE500
	CONCRETE WASHOUT PIT	NCG01 / CE503
	FUTURE PHASE 2 & 3	N/A


SITE LEGEND	
---	PROPERTY BOUNDARY
---	NEUSE RIVER BUFFER ZONE 1
---	NEUSE RIVER BUFFER ZONE 2
---	RIGHT-OF-WAY
---	LIMITS OF DISTURBANCE
---	WETLANDS

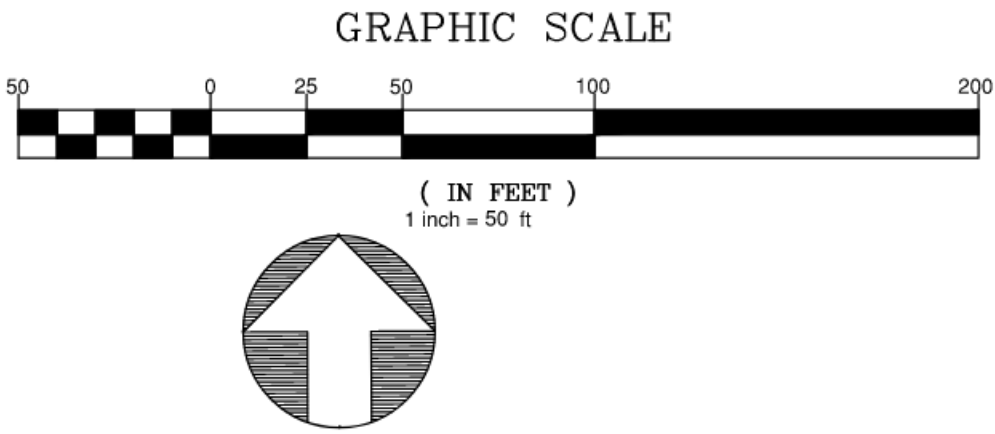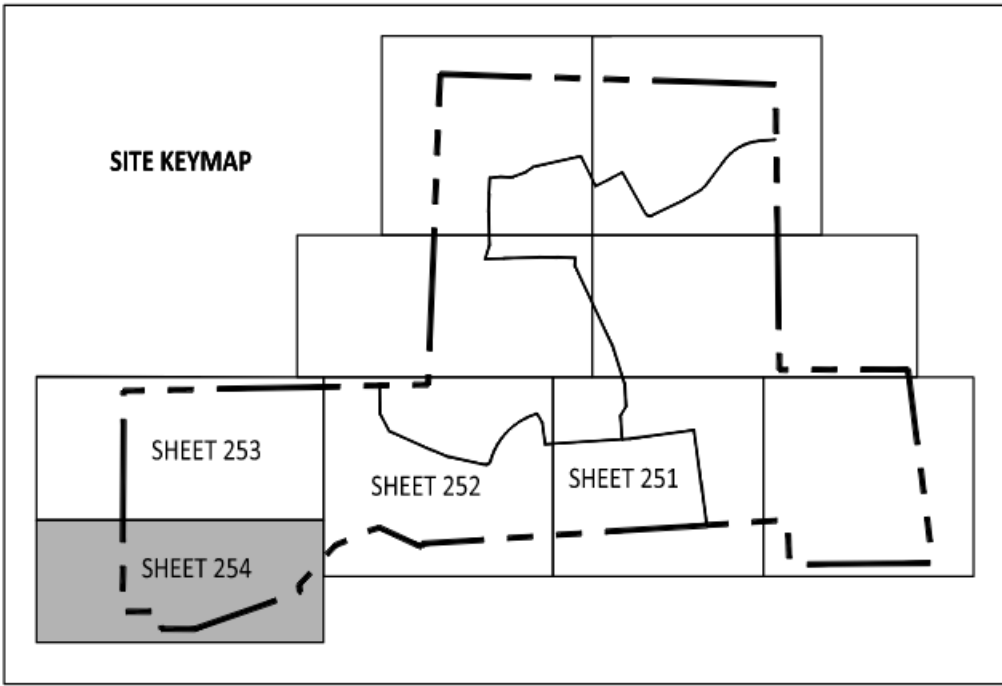

GENERAL NOTES:
1. ROLLED EROSION CONTROL PRODUCT (RECP) SHALL BE INSTALLED WHERE THE DIFFERENCE IN ELEVATION IS GREATER THAN 10 FT, WITHIN BASINS, AND WHERE SLOPES ARE GREATER THAN 3:1.



PROJECT NUMBER = CID-25-02

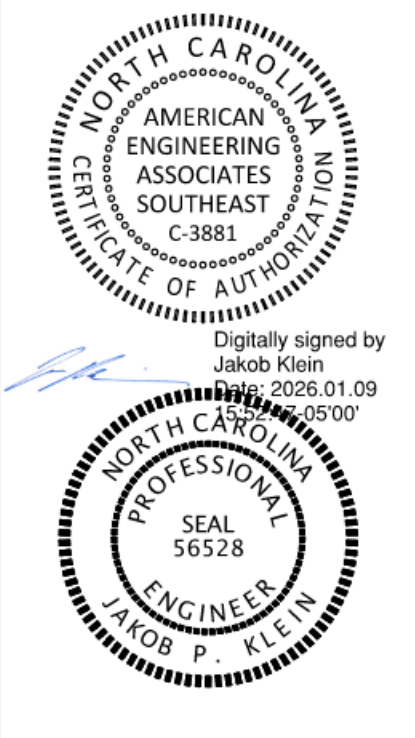

NO.	DATE	REVISION:

STIPULATION FOR REUSE
THIS DRAWING WAS PREPARED FOR USE ON THE SPECIFIC SITE, NAMED HEREON, CONTEMPORANEOUSLY WITH ITS ISSUE DATE AS LISTED, HEREON, AND IT IS NOT SUITABLE FOR USE ON A DIFFERENT PROJECT SITE OR AT A LATER TIME. USE OF THIS DRAWING FOR REFERENCE OR EXAMPLE ON ANOTHER PROJECT REQUIRES THE SERVICES OF PROPERLY LICENSED ARCHITECTS AND ENGINEERS. REPRODUCTION OF THIS DRAWING FOR REUSE ON ANOTHER PROJECT IS NOT AUTHORIZED AND MAY BE CONTRARY TO THE LAW.

MERRITT RESERVE
EROSION CONTROL
PHASE 3 STAGE 1
ROLESVILLE RD
WAKE COUNTY NC 27312

JOB NUMBER:	23-0004
CHECKED BY:	JK
DRAWN BY:	DH/MA/LL
DATE:	12/12/2025

SHEET TITLE:
EROSION CONTROL PHASE 3 STAGE 1
SHEET NO.:
CE-253

PLAN VIEW

SECTION VIEW

NOTES:

1. PLACE GRAVEL BAG BARRIER ON GENTLY SLOPING STREET, WHERE WATER CAN POND AND ALLOW SEDIMENT TO SEPARATE FROM RUNOFF.
2. USE SAND BAGS OF WOVEN GEOTEXTILE FABRIC (NOT BURLAP) AND FILL WITH 3/4 INCH (OR SMALLER) GRAVEL. BAGS MUST BE LAYERED SUCH THAT NO GAPS ARE EVIDENT.
3. WHEN INSTALLING CURB INLET PROTECTION DEVICES, NEVER BLOCK THE CURB INLET.

MAINTENANCE NOTES:

1. INSPECT BARRIERS AND REMOVE SEDIMENT AFTER EACH STORM EVENT (1 INCH OR GREATER). SEDIMENT AND GRAVEL MUST BE REMOVED FROM THE TRAVELED WAY IMMEDIATELY.

STANDARD GRAVEL BAG CURB INLET PROTECTION

01

EFFECTIVE: 01/31/08

PLAN VIEW

CROSS SECTION

NOTES:

1. INSTALL SILT FENCE OR TREE PROTECTION FENCE TO ENSURE CONSTRUCTION ENTRANCE IS USED BY VEHICLES.
2. IF MUD IS NOT REMOVED FROM TIRES AFTER VEHICLE TRAVELS OVER STONE, THE TIRES OF THE VEHICLE MUST BE WASHED BEFORE ENTERING PUBLIC ROADS.

MAINTENANCE NOTES:

1. THE GRAVEL CONSTRUCTION ENTRANCE MUST BE MAINTAINED IN A CONDITION TO PREVENT TRACKING OR DIRECT FLOW OF MUD ONTO ADJACENT ROADWAYS.
2. REPLACEMENT OF STONE MAY BE NECESSARY TO ENSURE THE GRAVEL ENTRANCE FUNCTIONS PROPERLY.
3. REPLENISHMENT OF STONE MAY BE NECESSARY.
4. FREQUENT CHECKS OF THE DEVICE AND TIMELY MAINTENANCE SHOULD BE COMPLETED.
5. ANY MATERIAL TRACKED ONTO THE ROADWAY SHALL BE CLEANED UP IMMEDIATELY.

STANDARD CONSTRUCTION ENTRANCE

02

EFFECTIVE: 01/31/08

SIDE VIEW

FRONT VIEW

STEP SEQUENCE

CONSTRUCTION NOTES:

1. HEIGHT & WIDTH DETERMINED BY EXISTING TOPOGRAPHY AND SEDIMENT STORAGE REQUIRED.
2. KEY RIP RAP INTO THE DAM FOR STABILIZATION.

MAINTENANCE NOTES:

1. INSPECT CHECK DAMS WEEKLY AND AFTER EVERY RAINFALL EVENT OF 1" OR MORE.
2. REMOVE SEDIMENT AND DEBRIS AS NEEDED.
3. MAINTAIN FLOW THROUGH THE CHECK DAM.

STANDARD CHECK DAM

03

EFFECTIVE: 01/31/08

PLAN VIEW

SECTION 'A-A'

MAINTENANCE NOTES:

1. REMOVE SEDIMENT WHEN HALF HEIGHT OF STONE AND CLEAR HARDWARE OF DEBRIS TO PROVIDE ADEQUATE FLOW FOR SUBSEQUENT RAINS. TAKING CARE NOT TO DAMAGE OR UNDERCUT HARDWARE DURING SEDIMENT REMOVAL.
2. REPLACE STONE AS NEEDED.

STANDARD GRAVEL YARD INLET PROTECTION

04

EFFECTIVE: 01/31/08

PLAN VIEW

CROSS SECTIONAL VIEW

NOTES:

- TO BE USED WHERE EXCESSIVE STORMWATER VELOCITIES PROHIBIT VEGETATIVE LININGS.
- SIZE OF STONE MUST BE DETERMINED BY APPROPRIATE DESIGN PROCEDURE.
- DIMENSIONS FOR d & W VARIES ACCORDING TO DESIGN.

MAINTENANCE NOTES:

1. INSPECT RIPRAP DITCH WEEKLY AND AFTER SIGNIFICANT RAIN EVENTS TO SEE IF ANY EROSION AROUND OR BELOW THE RIPRAP HAS TAKEN PLACE. IMMEDIATELY MAKE ALL NEEDED REPAIRS TO PREVENT FURTHER DAMAGE.
2. IF EROSION IS EVIDENT PAST END OF RIPRAP DITCH DUE TO RUNOFF DISCHARGING FROM DITCH, INCREASE DIMENSIONS OF RIPRAP PAD PROVIDED SPACE IS AVAILABLE WITHIN THE APPROVED LIMITS OF DISTURBANCE.
3. MAINTAIN ALL VEGETATION ADJACENT TO CHANNEL IN A HEALTHY, VIGOROUS CONDITION TO PROTECT DITCH FROM EROSION AND SCOUR DURING OUT-OF-BANK FLOW.

STANDARD RIP-RAP LINED CHANNELS

05

EFFECTIVE: 01/31/08

CROSS SECTIONAL VIEW

PLAN VIEW

NOTES:

1. TEMPORARY DIVERSION DITCH TO BE USED TO INTERCEPT FLOW AND/OR DIVERT TO A SEDIMENT CONTROL MEASURE OR BMP.
2. STABILIZE DIVERSION DITCH BERM WITH TEMPORARY SEEDING, MULCH WITH TAC, AND/OR EROSION CONTROL NETTING.

MAINTENANCE NOTES:

1. INSPECT ONCE A WEEK AND AFTER EVERY 1" RAINFALL.
2. SILT SHALL BE REMOVED WHEN DITCH IS ONE-HALF FULL.
3. DITCH SHALL BE RECONSTRUCTED WHEN DAMAGED BY EQUIPMENT OR COVERED BY FILL.
4. CHECK OUTLETS AND MAKE TIMELY REPAIRS AS NEEDED.
5. AFTER DRAINAGE AREA IS PERMANENTLY STABILIZED, PLACE WASTE MATERIAL IN DITCH TO BLEND WITH NATURAL GROUND AND STABILIZE.

STANDARD TEMPORARY DIVERSION DITCH

06

EFFECTIVE: 01/31/08

PLAN VIEW

SECTION 'A-A'

NOTES:

1. L = THE LENGTH OF THE RIPRAP APRON.
2. d = 1.5 TIMES THE MAXIMUM STONE DIAMETER BUT NOT LESS THAN 6" (INCHES).
3. A FILTER BLANKET OR FILTER FABRIC SHOULD BE INSTALLED BETWEEN THE RIPRAP AND SOIL FOUNDATION.

MAINTENANCE NOTES:

1. INSPECT RIPRAP OUTLET STRUCTURES WEEKLY AND AFTER SIGNIFICANT (1 INCH OR GREATER) RAINFALL EVENTS TO SEE IF ANY EROSION AROUND OR BELOW THE RIPRAP HAS TAKEN PLACE, OR IF STONES HAVE BEEN DISLODGED. IMMEDIATELY MAKE ALL NEEDED REPAIRS TO PREVENT FURTHER DAMAGE.

STANDARD PIPE OUTLET TO FLAT AREA NO WELL-DEFINED CHANNEL

07

EFFECTIVE: 01/31/08

PLAN VIEW

SECTION 'A-A'

NOTES:

1. L = THE LENGTH OF THE RIPRAP APRON.
2. d = 1.5 TIMES THE MAXIMUM STONE DIAMETER BUT NOT LESS THAN 6" (INCHES).
3. IN A WELL-DEFINED CHANNEL EXTEND THE APRON UP THE CHANNEL BANKS TO AN ELEVATION OF 6" (INCHES) ABOVE THE MAXIMUM TAILWATER DEPTH OR TO THE TOP OF THE BANK, WHICHEVER IS LESS.
4. A FILTER BLANKET OR FILTER FABRIC SHOULD BE INSTALLED BETWEEN THE RIPRAP AND SOIL FOUNDATION.

MAINTENANCE NOTES:

1. INSPECT RIPRAP OUTLET STRUCTURES WEEKLY AND AFTER SIGNIFICANT (1 INCH OR GREATER) RAINFALL EVENTS TO SEE IF ANY EROSION AROUND OR BELOW THE RIPRAP HAS TAKEN PLACE, OR IF STONES HAVE BEEN DISLODGED. IMMEDIATELY MAKE ALL NEEDED REPAIRS TO PREVENT FURTHER DAMAGE.

STANDARD PIPE OUTLET TO WELL-DEFINED CHANNEL

08

EFFECTIVE: 01/31/08

Cross-Section View

Plan View

MAINTENANCE NOTES:

1. CONSTRUCT THE ENTRANCE TO THE SLOPE DRAIN OF A STANDARD FLARED-END SECTION OF PIPE WITH A MINIMUM 6-INCH METAL TOE PLATE (CROSS-SECTION VIEW). MAKE ALL FITTINGS WATER-TIGHT. A STANDARD T-SECTION FITTING MAY ALSO BE USED AT THE INLET.
2. USE AN EARTHEN DIVERSION TO DIRECT SURFACE RUNOFF INTO THE TEMPORARY SLOPE DRAIN. MAKE THE HEIGHT OF THE BERM OVER THE DRAIN CONDUIT A MINIMUM OF 1.5 FT AND AT LEAST 6 INCHES HIGHER THAN THE ADJOINING BERM ON EITHER SIDE.
3. THE LOWEST POINT OF THE DIVERSION BERM SHOULD BE A MINIMUM OF 1 FT.
4. ABOVE THE TOP OF THE DRAIN SO THAT DESIGN FLOW CAN FREELY ENTER THE PIPE.
5. PROTECT THE OUTLET OF THE SLOPE DRAIN FROM EROSION WITH RIPRAP DISSEAL.
6. INSPECT SLOPE DRAINS AFTER EACH SIGNIFICANT RAINFALL OF 1 INCHES OR GREATER, OVER A 24-HOUR PERIOD.
7. REBUILD EARTH BERMS AND INLETS THAT HAVE WEAKENED DUE TO SCOURING.
8. EXTEND SLOPE DRAINS AND REBUILD INLET PROTECTION AS SLOPE IS BUILT, AFTER EACH 2-FOOT INCREASE IN HEIGHT.
9. REBUILD OR REPAIR SLOPE DRAINS IF NEEDED WHEN SEEDING AND MULCHING IS PERFORMED.
10. REBUILD OR REPAIR SLOPE DRAINS AS NEEDED.

STANDARD TEMPORARY SLOPE DRAIN

09

EFFECTIVE: 01/31/08


NO.	DATE	REVISION

STIPULATION FOR REUSE


THIS DRAWING WAS PREPARED FOR USE ON THE SPECIFIC SITE, NAMED HEREON, CONTEMPORANEOUSLY WITH ITS ISSUE DATE AS LISTED, HEREON, AND IT IS NOT SUITABLE FOR USE ON A DIFFERENT PROJECT SITE OR AT A LATER TIME. USE OF THIS DRAWING FOR REFERENCE OR EXAMPLE ON ANOTHER PROJECT REQUIRES THE SERVICES OF PROPERLY LICENSED ARCHITECTS AND ENGINEERS. REPRODUCTION OF THIS DRAWING FOR REUSE ON ANOTHER PROJECT IS NOT AUTHORIZED AND MAY BE CONTRARY TO THE LAW.

MERRITT RESERVE
EROSION CONTROL
DETAILS
ROLESVILLE RD
WAKE COUNTY NC 27312


JOB NUMBER:	23-0004
CHECKED BY:	JK
DRAWN BY:	DH/MA/LL
DATE:	12/12/2025
SHEET TITLE:	EROSION CONTROL DETAILS
SHEET NO.:	CE-500

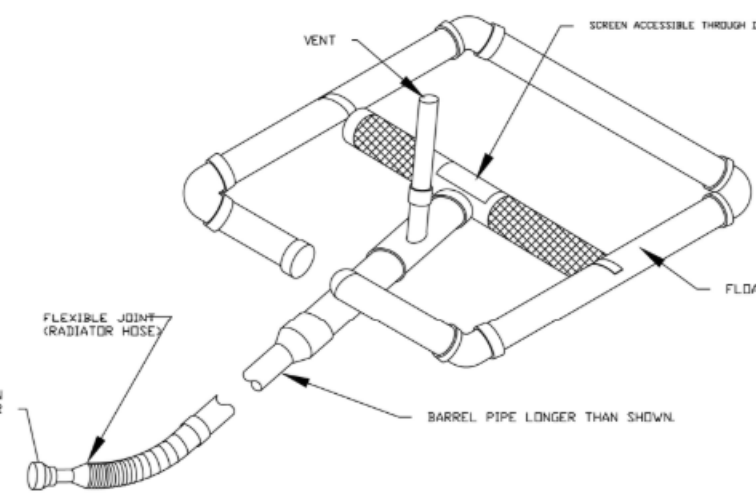

01

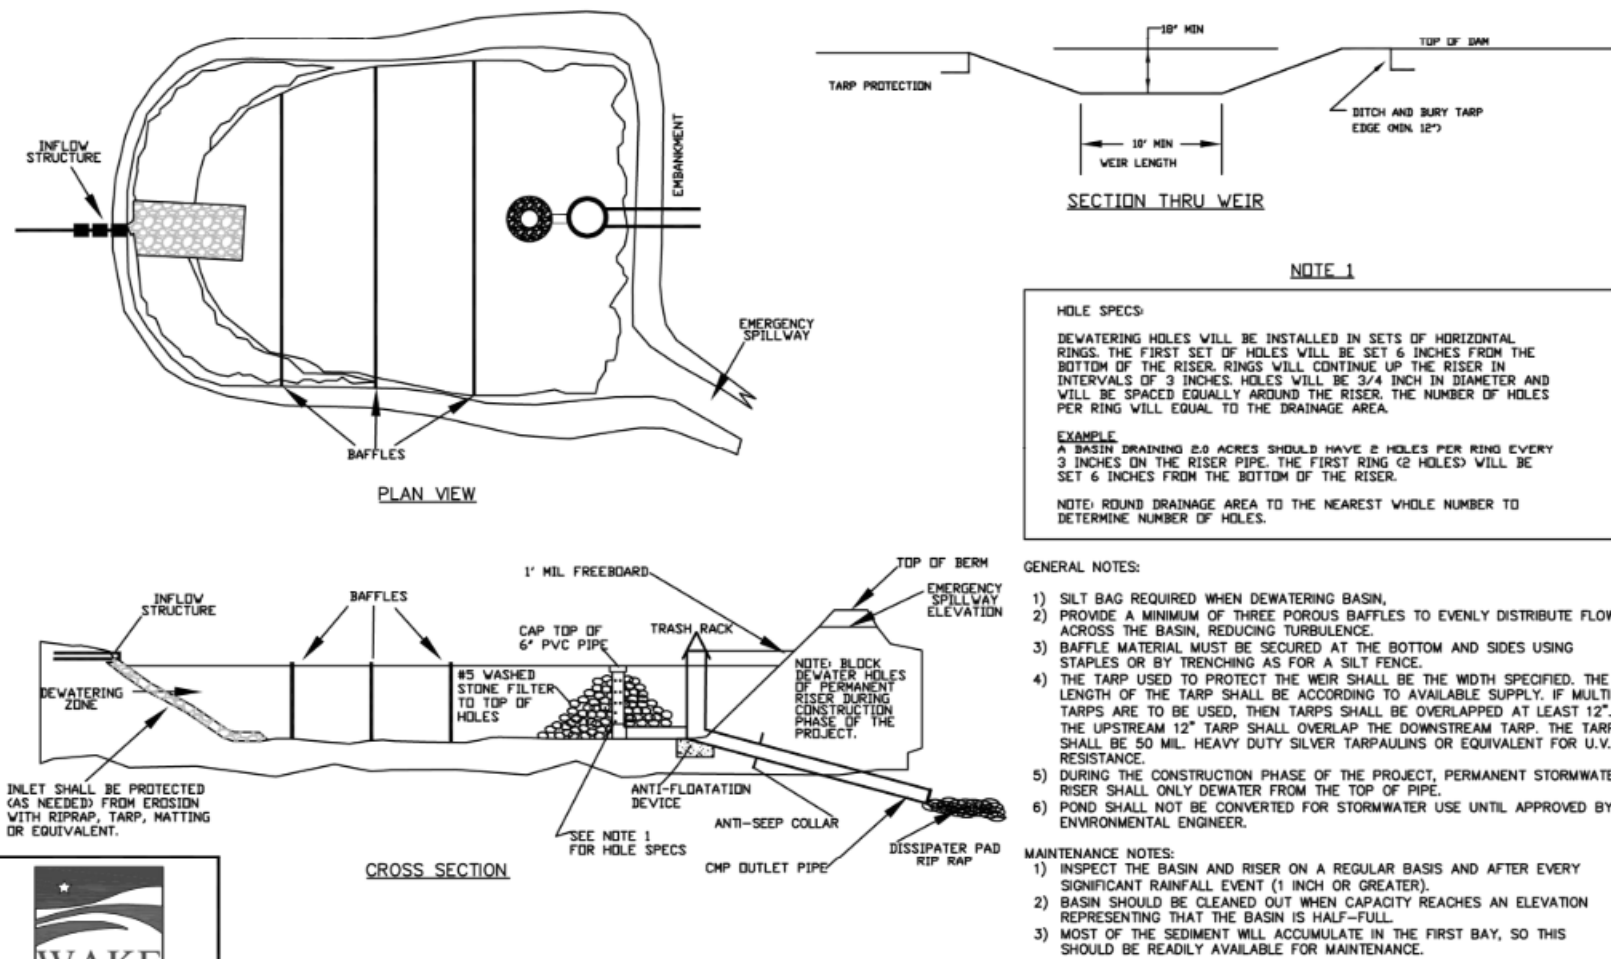


04

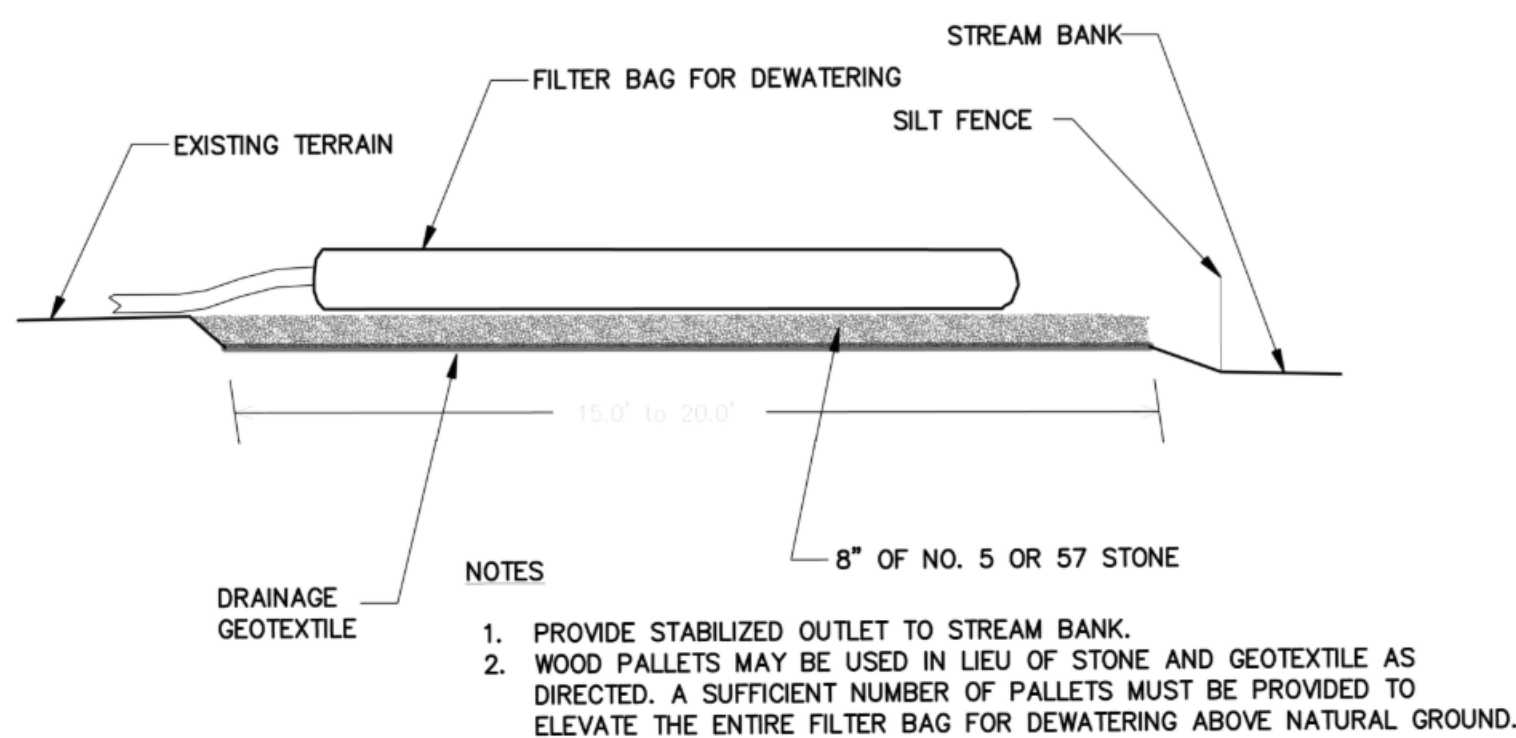


1. REPLACE AND DISPOSE OF FILTER BAG(S) WHEN IT IS $\frac{3}{4}$ FULL OF SEDIMENT OR WHEN IT IS IMPRACTICAL FOR BAG TO FILTER SEDIMENT.
2. PROVIDE A SUFFICIENT QUANTITY OF FILTER BAGS TO CONTAIN SILT FROM PUMPED EFFLUENT.


06

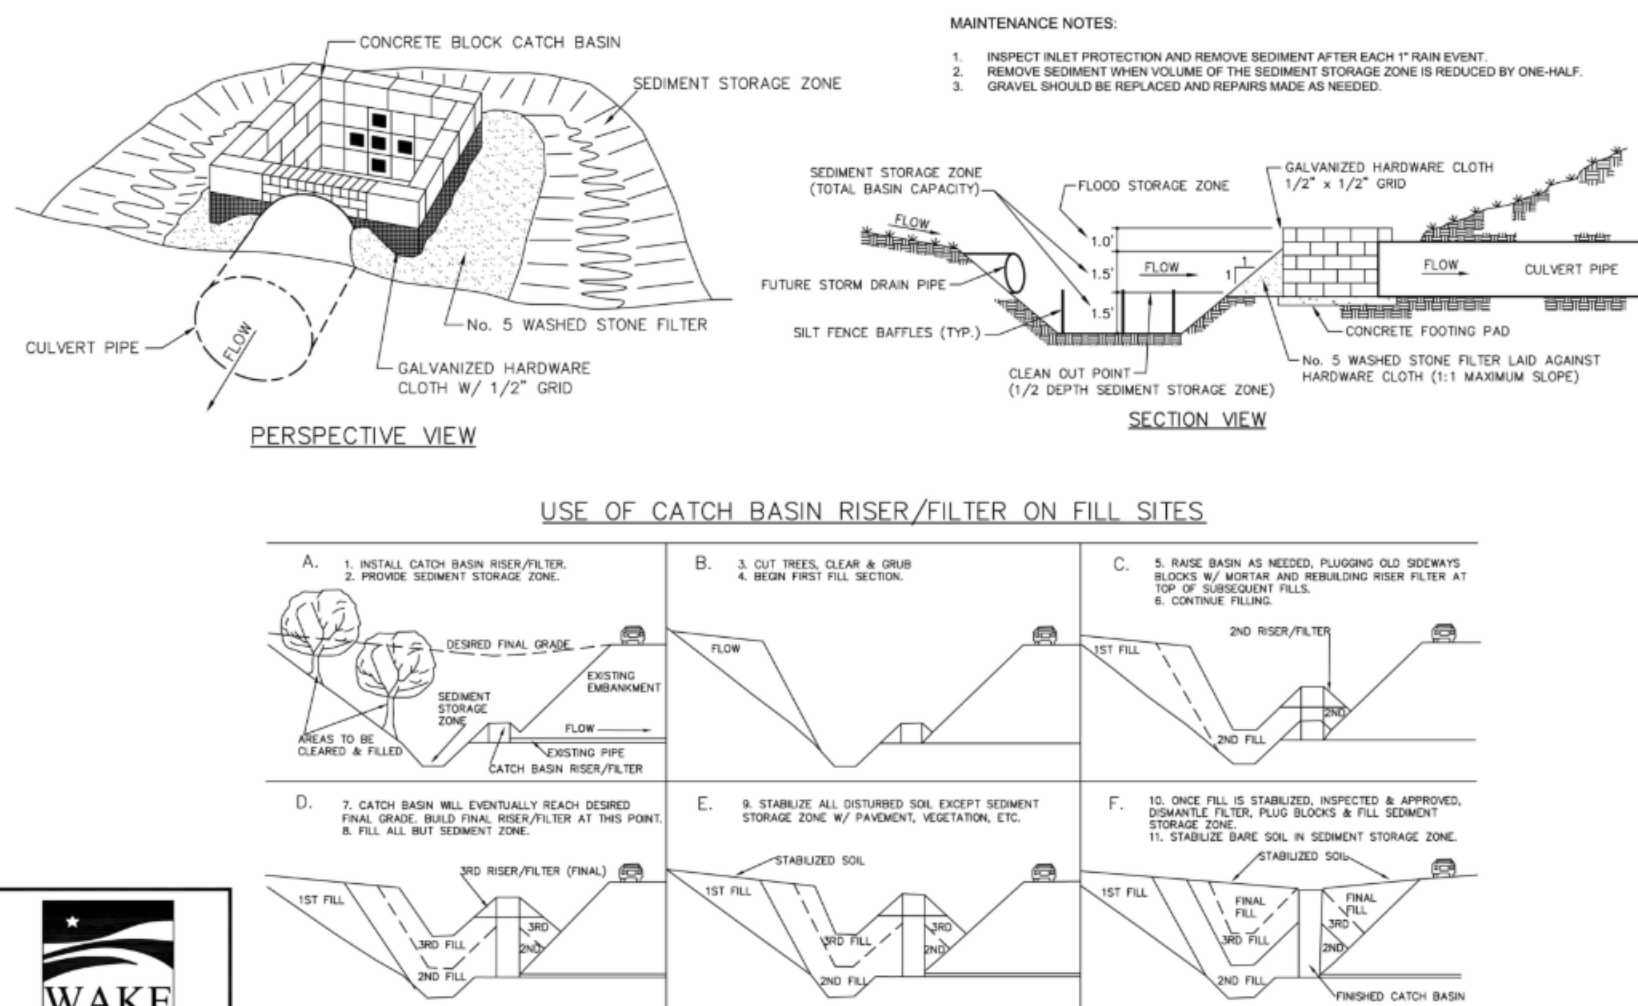


02

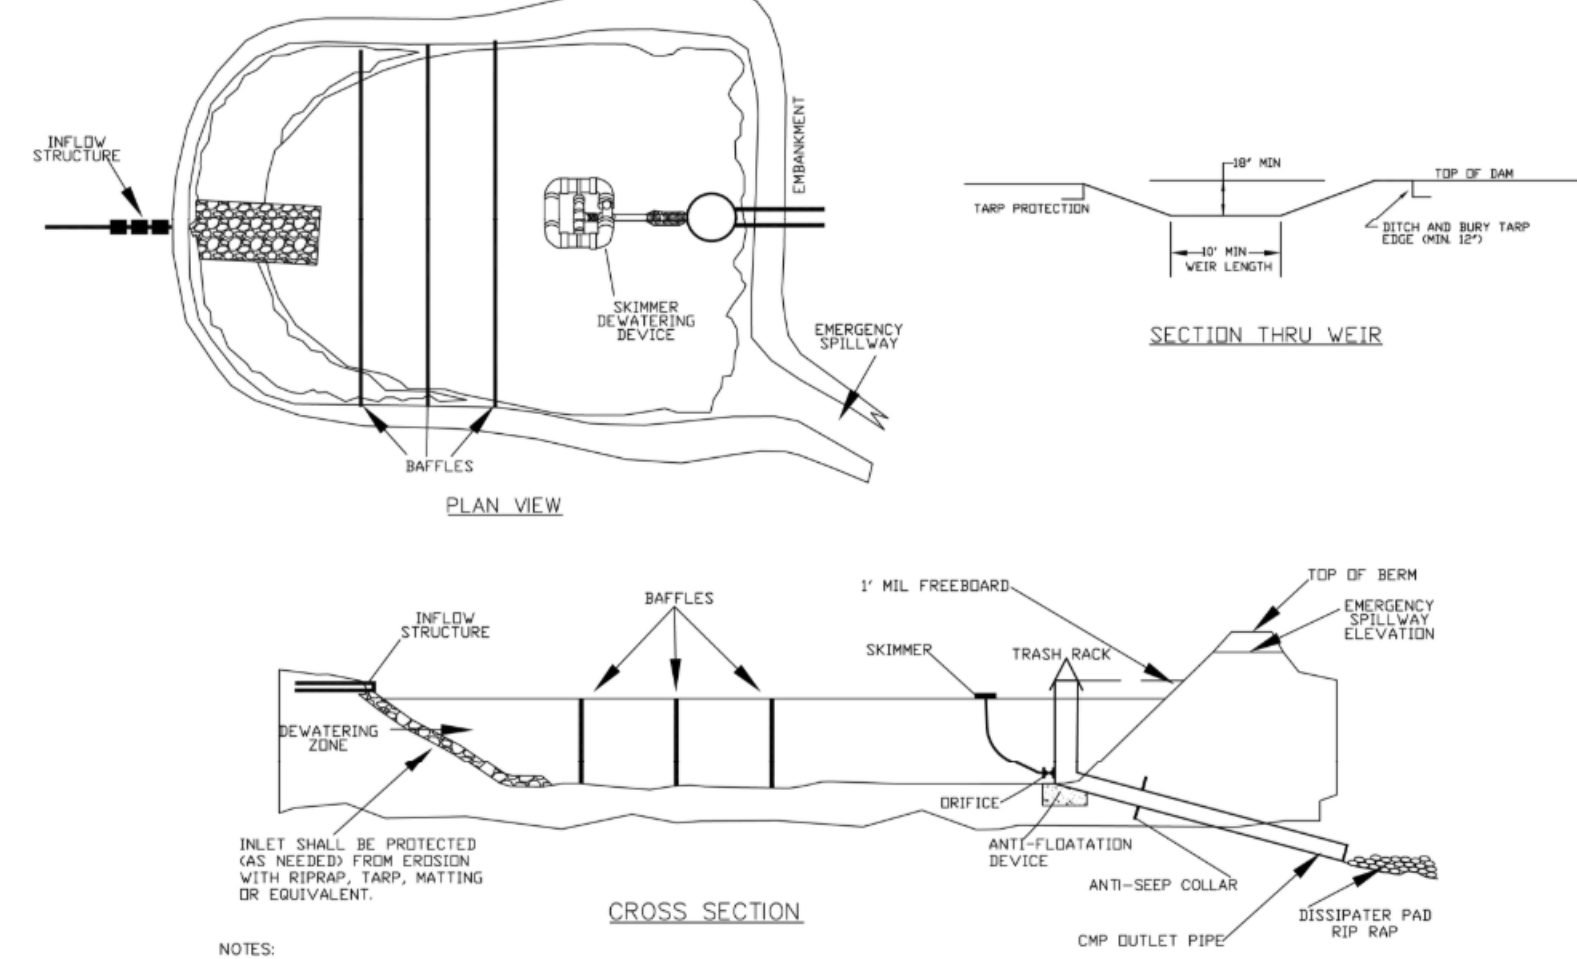

05

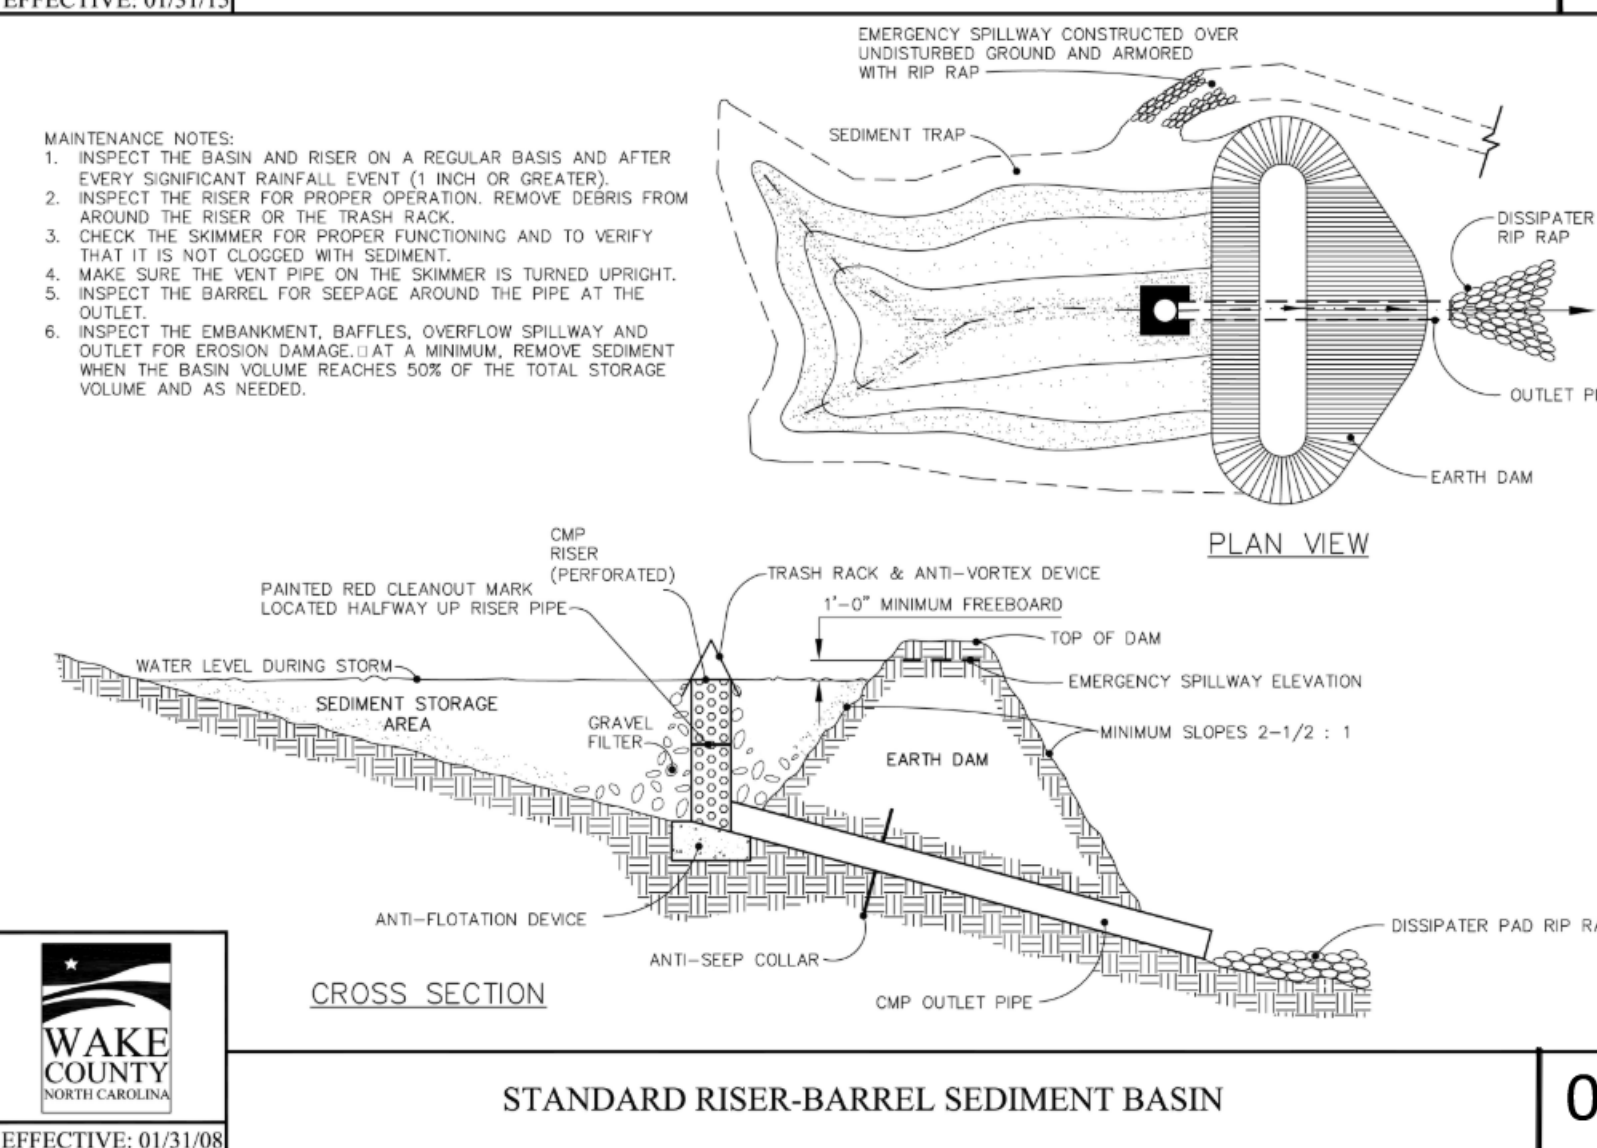

07

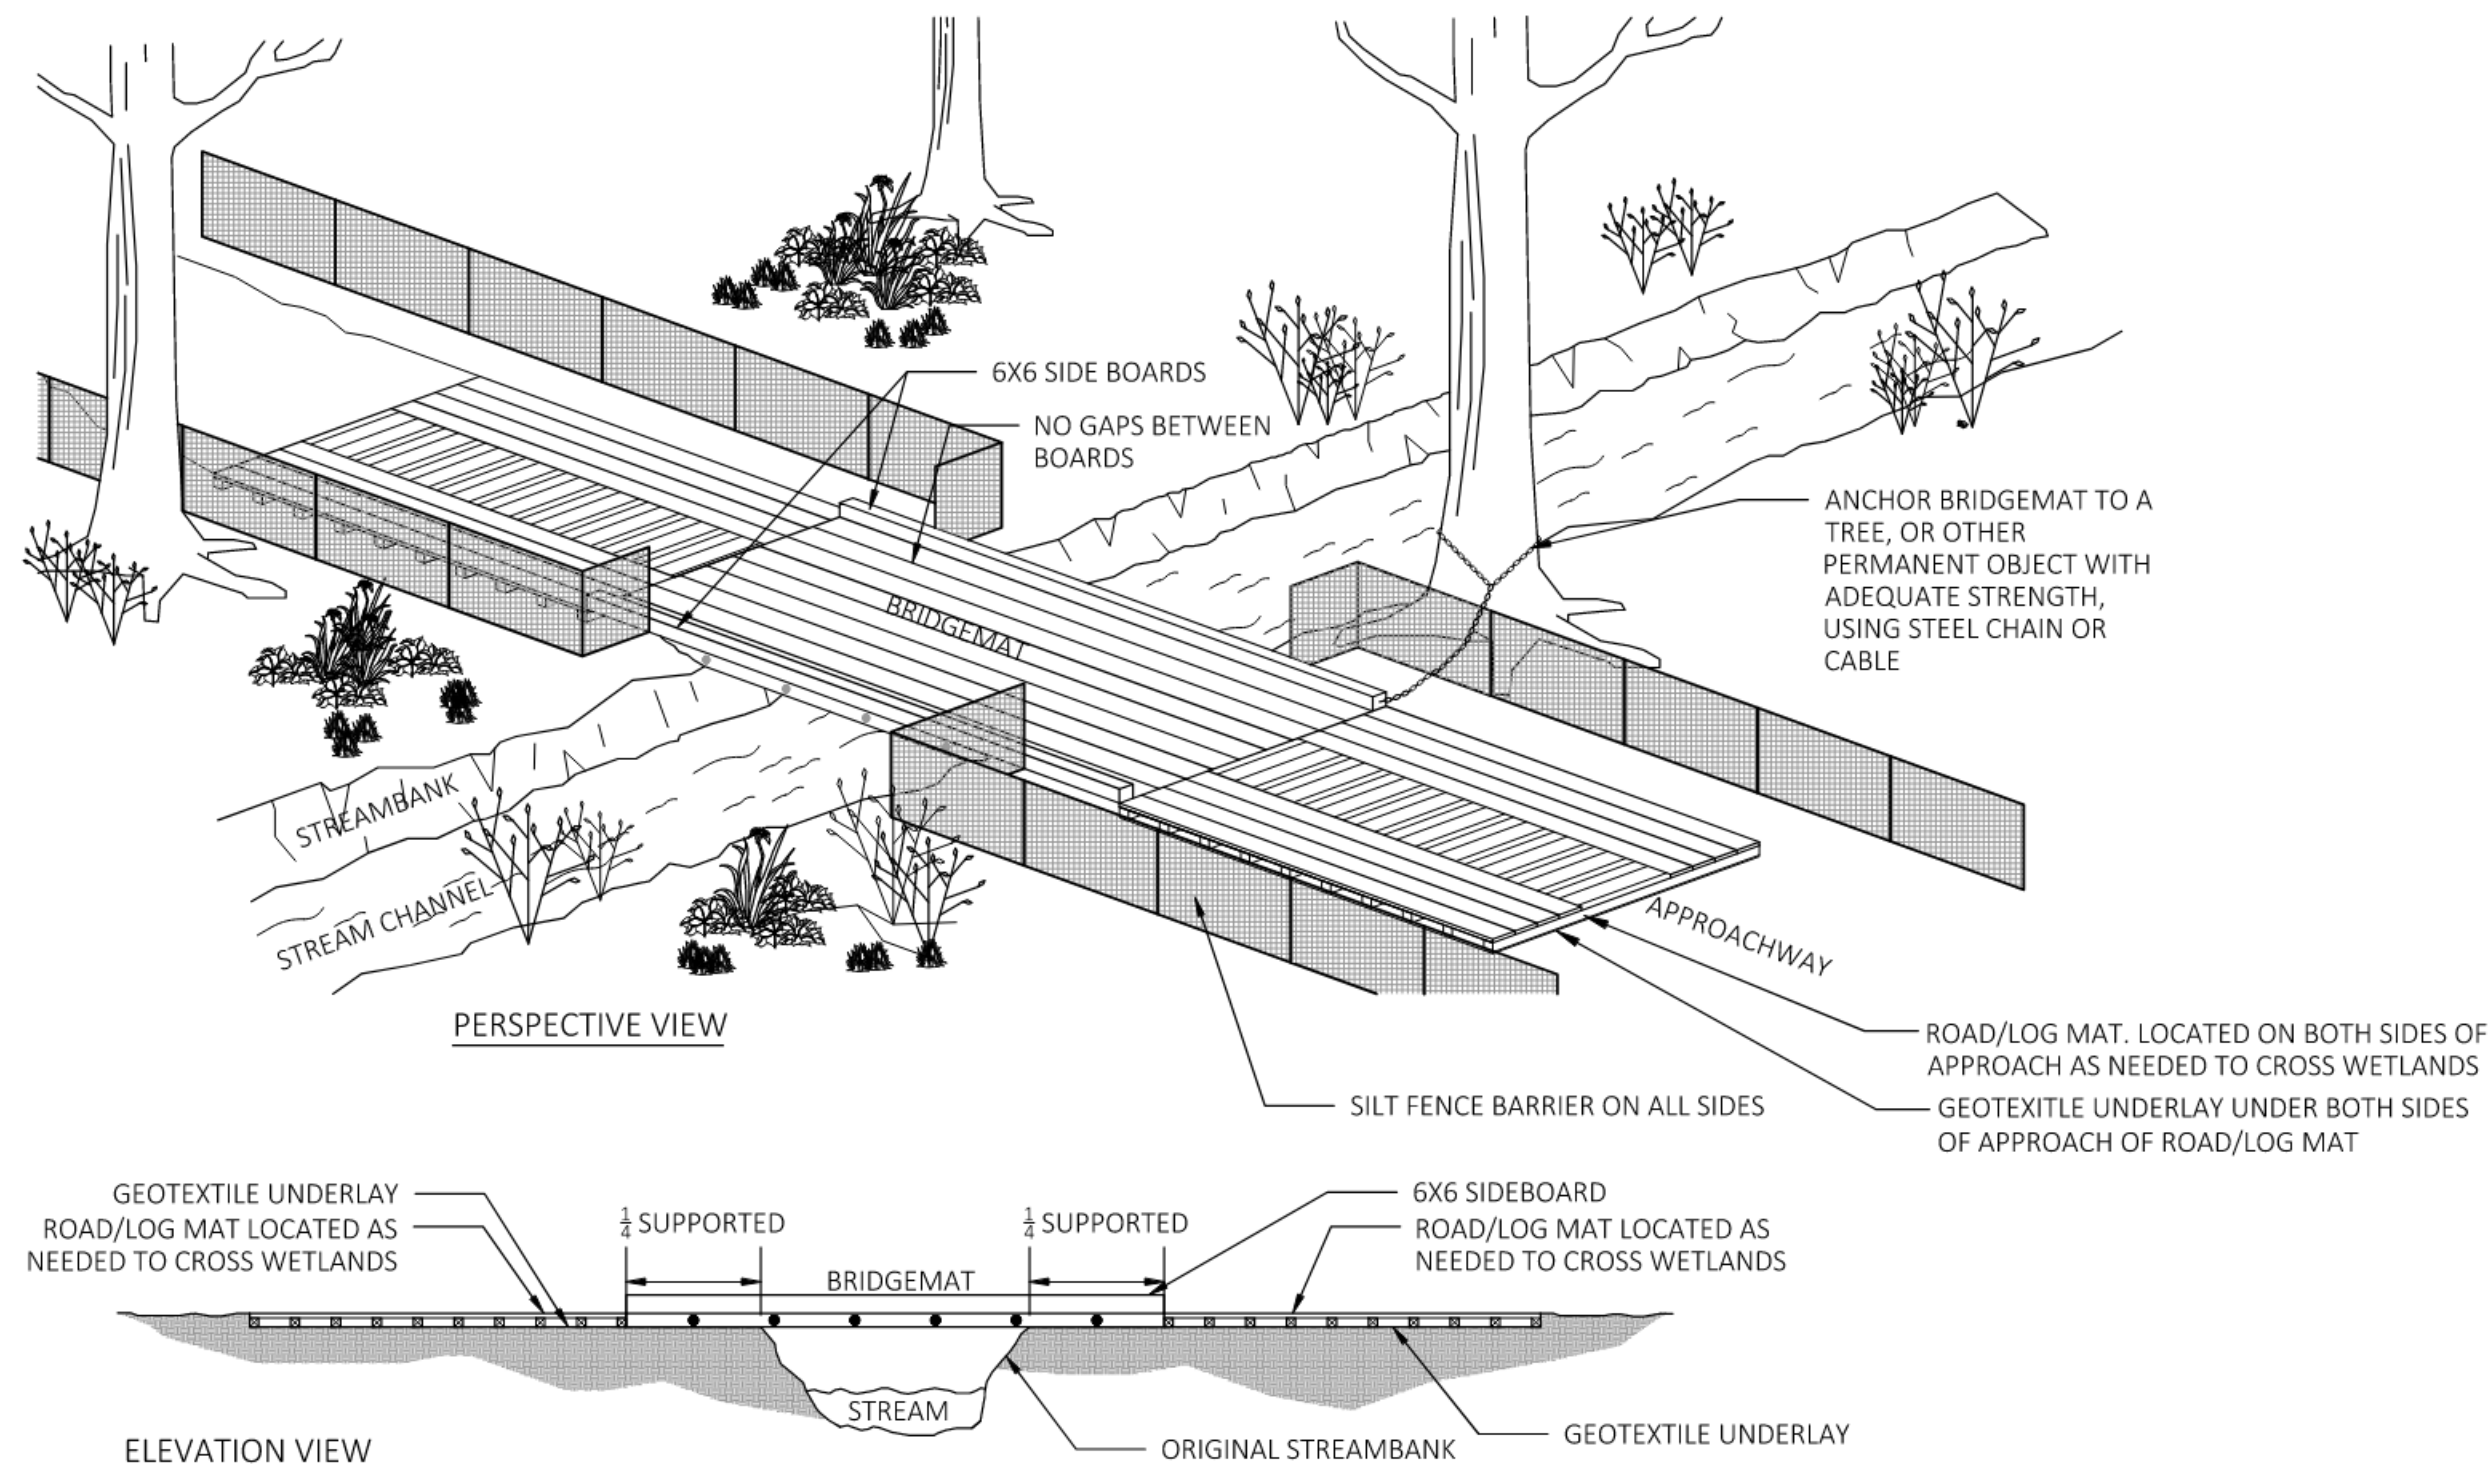


1. KEEP CLEARING AND EXCAVATION OF THE STREAM BANKS AND BED AND APPROACH TO A MINIMUM.
2. INSTALL AND MAINTAIN A SILT FENCE BARRIER AT ALL ALLEGEDLY DISTURBED APPROACHES INCLUDING ALONG STREAM BANK
3. KEEP HEAVY EQUIPMENT OUT OF STREAM AT ALL TIMES.
4. INSTALL ROAD/LOG MAT AT FINAL APPROACH TO BARRIER WITH GEOTEXTILE UNDERLAY.
5. MINIMIZE EXPOSURE OF STREAM SOIL WITH TREE TOPS OR BRUSH DURING MAT INSTALLATION, AND SEEDING/MULCH AFTER MAT REMOVAL.
6. INSTALL MATS TO CREATE A MINIMUM TEN FOOT BARRIER WIDTH.
7. SCHEDULE BRIDGE SECTION INSTALLATION FOR PERIOD OF DRY WEATHER. REMOVE SILT FENCE ALONG STREAM BANK ONLY AS NECESSARY TO ALLOW BRIDGE INSTALLATION AND REINSTALL SILT FENCE ALONG STREAM BANK TO EDGE OF BRIDGE FOLLOWING BRIDGE INSTALLATION.
8. INSTALL ROAD/LOG MATS ON OPPOSITE SIDE OF NEWLY INSTALLED BRIDGE. INSTALL AND MAINTAIN A SILT FENCE BARRIER ALONG ALL DISTURBED AREAS.

1. KEEP MATS' SURFACE FREE OF MINERAL SOIL AND DEBRIS THAT COULD ENTER STREAM.
2. PERIODICALLY CHECK MAT HARDWARE; RE-TIGHTEN NUTS AND CABLE CLAMPS AS NECESSARY TO MAINTAIN BRIDGE STRENGTH AND INTEGRITY.
3. CHECK AND MAINTAIN SILT FENCE BARRIERS ON A DAILY BASIS.
4. IMMEDIATELY REMOVE ANY DEBRIS WHICH ENTERS THE STREAM AT THE CROSSING LOCATION.

1. CLEAN OFF BRIDGE SURFACE.
2. REMOVE MATS BY USING MAT CABLE LOOP OR SKIDDER GRAPPLE.
3. PERMANENTLY STABILIZE DISTURBED PORTIONS OF STREAM BANK AND APPROACH ROADS WITH MULCH.

NOT TO SCALE

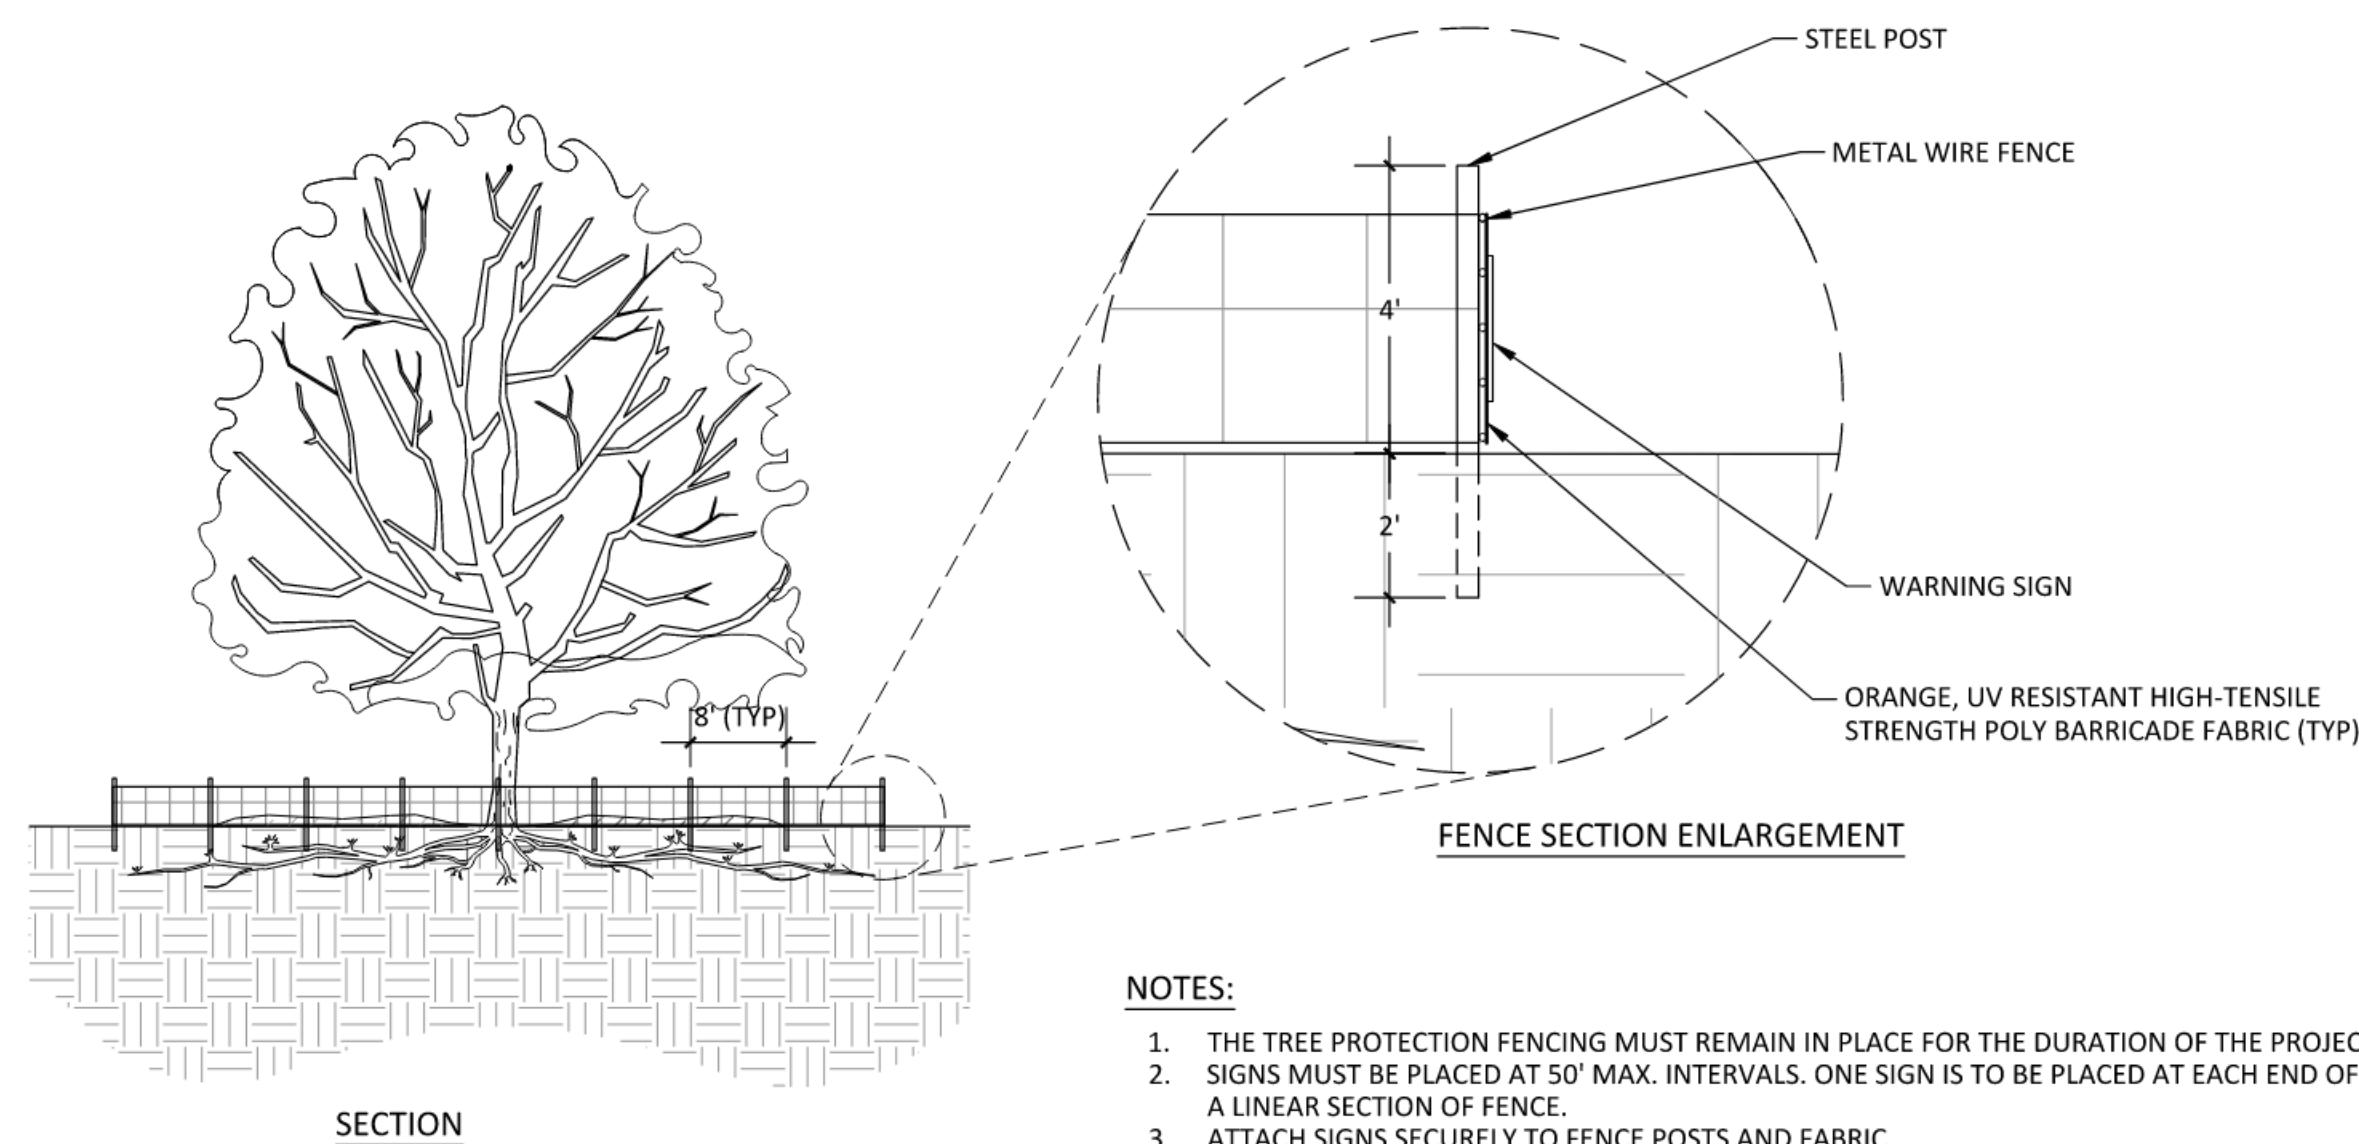


1. THE TREE PROTECTION FENCING MUST REMAIN IN PLACE FOR THE DURATION OF THE PROJECT.
2. SIGNS MUST BE PLACED AT 50' MAX. INTERVALS. ONE SIGN IS TO BE PLACED AT EACH END OF A LINEAR SECTION OF FENCE.
3. ATTACH SIGNS SECURELY TO FENCE POSTS AND FABRIC.
4. SIGNS ARE TO BE MADE OF DURABLE AND WEATHERPROOF MATERIAL WITH CLEARLY LEGIBLE LETTERS.
5. TREE PROTECTION FENCE IS TO BE REMOVED ONCE CONSTRUCTION IS COMPLETE.

NOT TO SCALE

P-RE-R-R230004-03

North Carolina 811
*** 3 Days Before Digging ***
North Carolina 811
811 or 1-800-632-4949
Remote Ticket Entry
<http://nc811.org/remoteticketentry.htm>

PROJECT NUMBER = CID-25-02



AMERICAN
Engineering

American Engineering Associates - Southeast, P.A.
4020 Westchase Boulevard, Suite 450
Raleigh, NC 27607
919-469-1101



NORTH CAROLINA
ENGINEERING
ASSOCIATES
SOUTHEAST
C-3881

Digitally signed by
Jakob Klein
Date: 2026.01.09

[illegible]

STIPULATION FOR REUSE

THIS DRAWING WAS PREPARED FOR USE ON THE SPECIFIC SITE, NAMED HEREON, CONTEMPORANEOUSLY WITH ITS ISSUANCE AS LISTED, HEREON, AND IT IS NOT SUITABLE FOR USE ON A DIFFERENT PROJECT SITE OR AT A LATER TIME. USE OF THIS DRAWING FOR REFERENCE OR EXAMPLE ON ANOTHER PROJECT REQUIRES THE SERVICES OF PROPERLY LICENSED ARCHITECTS AND ENGINEERS. REPRODUCTION OF THIS DRAWING FOR REUSE ON ANOTHER PROJECT IS NOT AUTHORIZED AND MAY BE CONTRARY TO THE LAW.

P-RE-R-R230004-04

**MERRITT RESERVE
EROSION CONTROL
DETAILS**
ROLESVILLE RD
WAKE COUNTY NC 27312

JOB NUMBER:	23-0004
CHECKED BY:	JD

DRAWN BY:	DH/MA/L
DATE:	12/12/200

© 1997 by The McGraw-Hill Companies, Inc.

EROSION CONTROL DETAILS

SHEET NO.: **CE-502**

GROUND STABILIZATION AND MATERIALS HANDLING PRACTICES FOR COMPLIANCE WITH THE NCG01 CONSTRUCTION GENERAL PERMIT

Implementing the details and specifications on this plan sheet will result in the construction activity being considered compliant with the Ground Stabilization and Materials Handling sections of the NCG01 Construction General Permit (Sections E and F, respectively). The permittee shall comply with the Erosion and Sediment Control plan approved by the delegated authority having jurisdiction. All details and specifications shown on this sheet may not apply depending on site conditions and the delegated authority having jurisdiction.

SECTION E: GROUND STABILIZATION

Required Ground Stabilization Timeframes		
Site Area Description	Stabilize within this many calendar days after ceasing land disturbance	Timeframe variations
(a) Perimeter dikes, swales, ditches, and perimeter slopes	7	None
(b) High Quality Water (HQW) Zones	7	None
(c) Slopes steeper than 3:1	7	If slopes are 10' or less in length and are not steeper than 2:1, 14 days are allowed
(d) Slopes 3:1 to 4:1	14	-7 days for slopes greater than 50' in length and with slopes steeper than 4:1 -7 days for perimeter dikes, swales, ditches, perimeter slopes and HQW Zones -10 days for Falls Lake Watershed
(e) Areas with slopes flatter than 4:1	14	-7 days for perimeter dikes, swales, ditches, perimeter slopes and HQW Zones -10 days for Falls Lake Watershed unless there is zero slope

Note: After the permanent cessation of construction activities, any areas with temporary ground stabilization shall be converted to permanent ground stabilization as soon as practicable but in no case longer than 90 calendar days after the last land disturbing activity. Temporary ground stabilization shall be maintained in a manner to render the surface stable against accelerated erosion until permanent ground stabilization is achieved.

GROUND STABILIZATION SPECIFICATION

Stabilize the ground sufficiently so that rain will not dislodge the soil. Use one of the techniques in the table below.

Temporary Stabilization	Permanent Stabilization
- Temporary grass seed covered with straw or other mulches and tackifiers - Hydroseeding - Roll-on erosion control products with or without temporary grass seed - Appropriately applied straw or other mulch - Plastic sheeting	- Permanent grass seed covered with straw or other mulches and tackifiers - Geotextile fabrics such as permanent soil reinforcement matting - Hydroseeding - Shrubs or other permanent plantings covered with mulch - Uniform and evenly distributed ground cover sufficient to restrain erosion - Structural methods such as concrete, asphalt or retaining walls - Roll-on erosion control products with grass seed

POLYACRYLAMIDES (PAMS) AND FLOCCULANTS

- Select flocculants that are appropriate for the soils being exposed during construction, selecting from the NC DWR List of Approved PAMS/Flocculants.
- Apply flocculants at or before the inlets to Erosion and Sediment Control Measures.
- Apply flocculants at the concentrations specified in the NC DWR List of Approved PAMS/Flocculants and in accordance with the manufacturer's instructions.
- Provide ponding area for containment of treated Stormwater before discharging offsite.
- Store flocculants in leak-proof containers that are kept under storm-resistant cover or surrounded by secondary containment structures.

EQUIPMENT AND VEHICLE MAINTENANCE

- Maintain vehicles and equipment to prevent discharge of fluids.
- Provide drip pans under any stored equipment.
- Identify leaks and repair as soon as feasible, or remove leaking equipment from the project.
- Collect all spent fluids, store in separate containers and properly dispose as hazardous waste (recycle when possible).
- Remove leaking vehicles and construction equipment from service until the problem has been corrected.
- Bring used fuels, lubricants, coolants, hydraulic fluids and other petroleum products to a recycling or disposal center that handles these materials.

LITTER, BUILDING MATERIAL AND LAND CLEARING WASTE

- Never bury or burn waste. Place litter and debris in approved waste containers.
- Provide a sufficient number and size of waste containers (e.g. dumpster, trash receptacle) on site to contain construction and domestic wastes.
- Locate waste containers at least 50 feet away from storm drain inlets and surface waters unless no other alternatives are reasonably available.
- Locate waste containers on areas that do not receive substantial amounts of runoff from upland areas and does not drain directly to a storm drain, stream or wetland.
- Cover waste containers at the end of each workday and before storm events or provide secondary containment. Repair or replace damaged waste containers.
- Anchor all lightweight items in waste containers during times of high winds.
- Empty waste containers as needed to prevent overflow. Clean up immediately if containers overflow.
- Dispose waste off-site at an approved disposal facility.
- On business days, clean up and dispose of waste in designated waste containers.

PAINT AND OTHER LIQUID WASTE


- Do not dump paint and other liquid waste into storm drains, streams or wetlands.
- Locate paint washouts at least 50 feet away from storm drain inlets and surface waters unless no other alternatives are reasonably available.
- Contain liquid wastes in a controlled area.
- Containment must be labeled, sized and placed appropriately for the needs of site.
- Prevent the discharge of soaps, solvents, detergents and other liquid wastes from construction sites.

PORTABLE TOILETS

- Install portable toilets on level ground, at least 50 feet away from storm drains, streams or wetlands unless there is no alternative reasonably available. If 50 foot offset is not attainable, provide relocation of portable toilet behind silt fence or place on a gravel pad and surround with sand bags.
- Provide staking or anchoring of portable toilets during periods of high winds or in high foot traffic areas.
- Monitor portable toilets for leaking and properly dispose of any leaked material. Utilize a licensed sanitary waste hauler to remove leaking portable toilets and replace with properly operating unit.

EARTHEN STOCKPILE MANAGEMENT

- Show stockpile locations on plans. Locate earthen-material stockpile areas at least 50 feet away from storm drain inlets, sediment basins, perimeter sediment controls and surface waters unless it can be shown no other alternatives are reasonably available.
- Protect stockpile with silt fence installed along toe of slope with a minimum offset of five feet from the toe of stockpile.
- Provide stable stone access point when feasible.
- Stabilize stockpile within the timeframes provided on this sheet and in accordance with the approved plan and any additional requirements. Soil stabilization is defined as vegetative, physical or chemical coverage techniques that will restrain accelerated erosion on disturbed soils for temporary or permanent control needs.

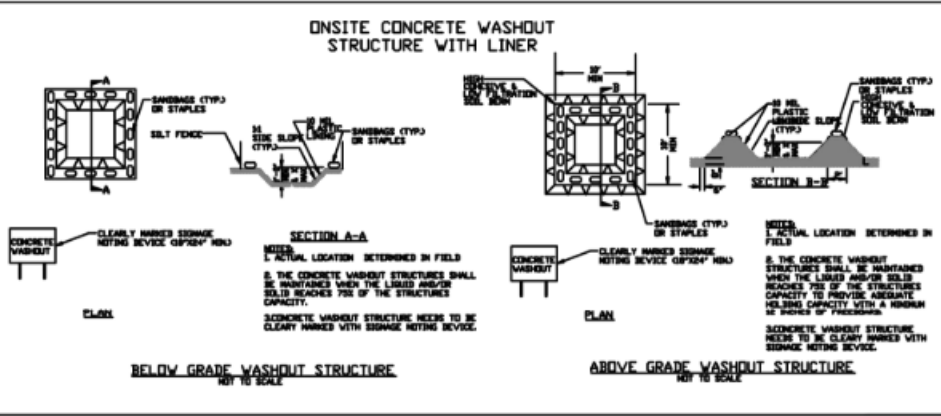

CONCRETE WASHOUTS


- Do not discharge concrete or cement slurry from the site.
- Dispose of, or recycle settled, hardened concrete residue in accordance with local and state solid waste regulations and at an approved facility.
- Manage washout from mortar mixers in accordance with the above item and in addition place the mixer and associated materials on impervious barrier and within lot perimeter silt fence.
- Install temporary concrete washouts per local requirements, where applicable. If an alternate method or product is to be used, contact your approval authority for review and approval. If local standard details are not available, use one of the two types of temporary concrete washouts provided on this detail.
- Do not use concrete washouts for dewatering or storing defective curb or sidewalk sections. Stormwater accumulated within the washout may not be pumped into or discharged to the storm drain system or receiving surface waters. Liquid waste must be pumped out and removed from project.
- Locate washouts at least 50 feet from storm drain inlets and surface waters unless it can be shown that no other alternatives are reasonably available. At a minimum, install protection of storm drain inlet(s) closest to the washout which could receive spills or overflow.
- Locate washouts in an easily accessible area, on level ground and install a stone entrance pad in front of the washout. Additional controls may be required by the approving authority.
- Install at least one sign directing concrete trucks to the washout within the project limits. Post signage on the washout itself to identify this location.
- Remove leavings from the washout when at approximately 75% capacity to limit overflow events. Replace the tarp, sand bags or other temporary structural components when no longer functional. When utilizing alternative or proprietary products, follow manufacturer's instructions.
- At the completion of the concrete work, remove remaining leavings and dispose of in an approved disposal facility. Fill pit, if applicable, and stabilize any disturbance caused by removal of washout.

HERBICIDES, PESTICIDES AND RODENTICIDES

- Store and apply herbicides, pesticides and rodenticides in accordance with label restrictions.
- Store herbicides, pesticides and rodenticides in their original containers with the label, which lists directions for use, ingredients and first aid steps in case of accidental poisoning.
- Do not store herbicides, pesticides and rodenticides in areas where flooding is possible or where they may spill or leak into wells, stormwater drains, ground water or surface water. If a spill occurs, clean area immediately.
- Do not stockpile these materials onsite.

HAZARDOUS AND TOXIC WASTE

- Create designated hazardous waste collection areas on-site.
- Place hazardous waste containers under cover or in secondary containment.
- Do not store hazardous chemicals, drums or bagged materials directly on the ground.

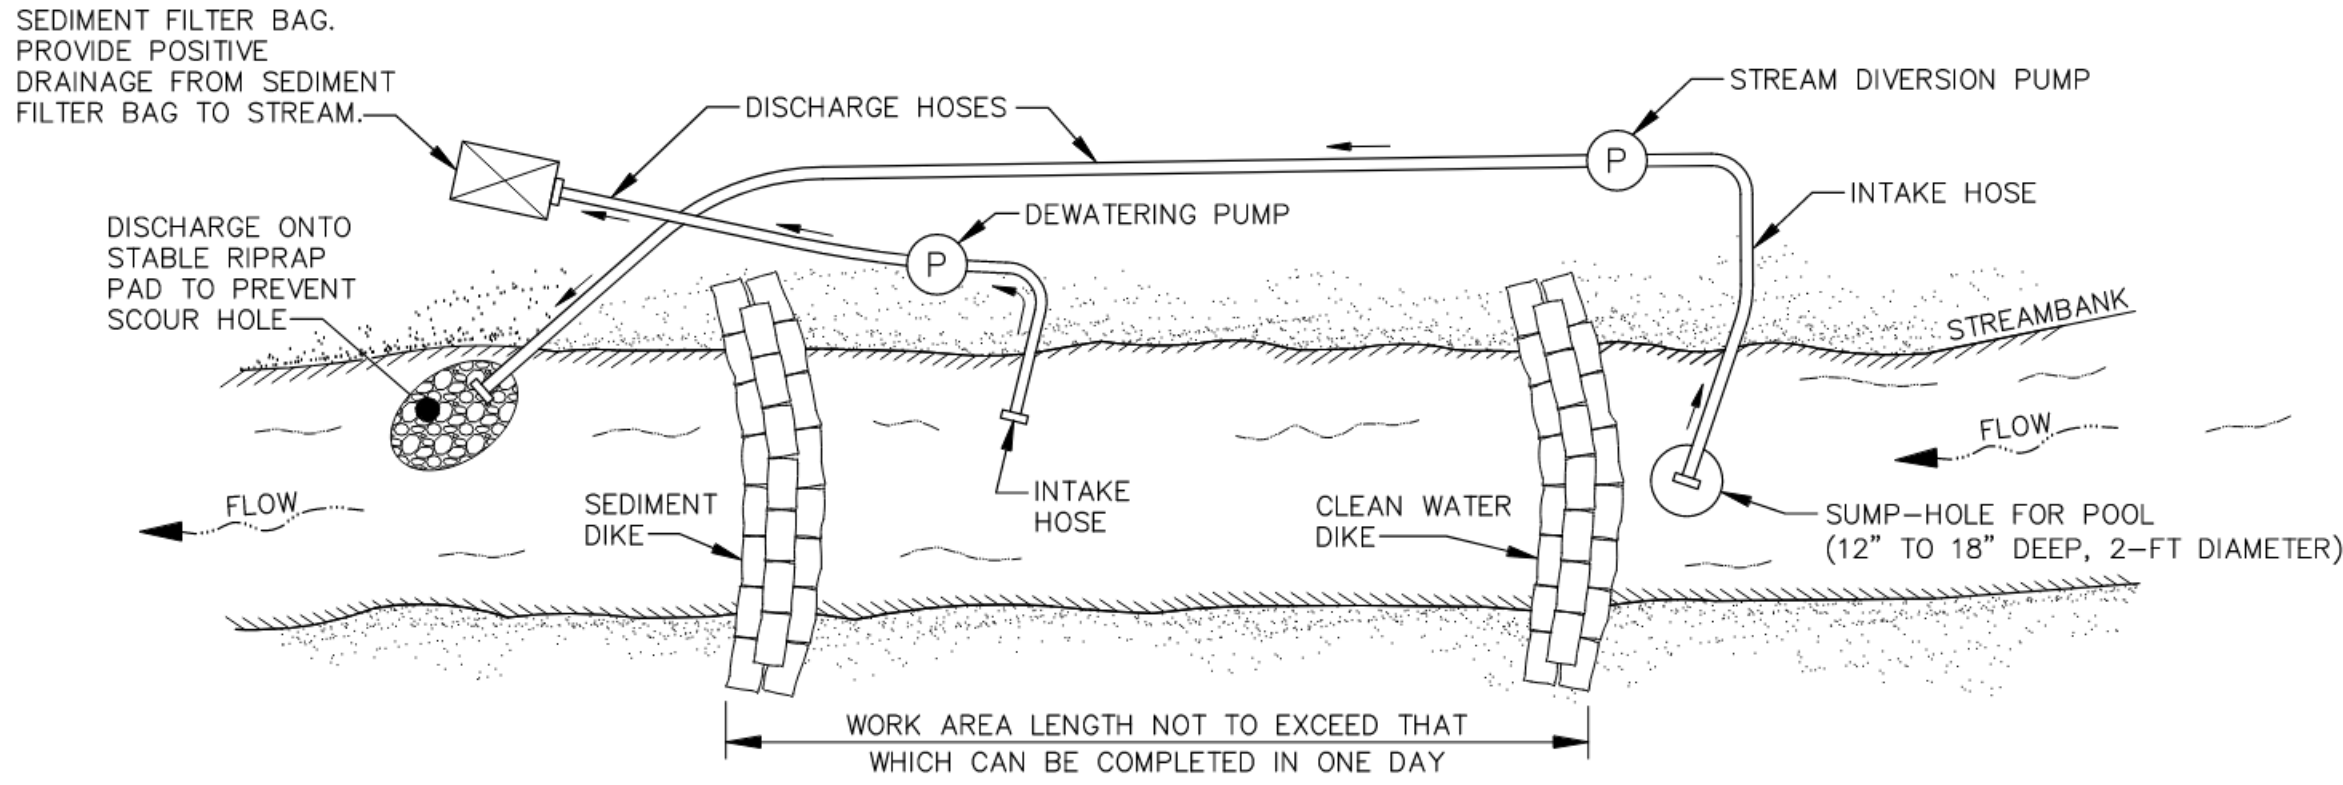

MAINTENANCE NOTES:

- INITIAL SETUP OF BYPASS PUMPING SHOULD BE PERFORMED WHEN 3-4 DAYS OF DRY WEATHER IS FORECASTED.
- INSPECT STREAM DIVERSION DAILY. CORRECT ANY DEFICIENCIES IMMEDIATELY.
- AREAS ADJACENT TO WORK AREA SHOULD BE STABILIZED.

TEMPORARY PUMP AROUND SEQUENCE

- SET UP PUMP WITH SUCTION AND DISCHARGE HOSE.
- INSTALL UP-STREAM SANDBAG DAM.
- INSTALL DOWN-STREAM SANDBAG DAM.
- THE PUMP MUST RUN CONTINUOUSLY WHILE WORKING IN THE STREAM.
- STREAM BANKS MUST BE STABILIZED AT THE END OF EACH DAY.

GENERAL NOTES:

- DIKES SHALL BE SITUATED AT THE UPSTREAM AND DOWNSTREAM ENDS OF THE WORK AREA, AND STREAM FLOW SHALL BE PUMPED AROUND THE WORK AREA. THE PUMP SHOULD DISCHARGE ONTO A STABLE VELOCITY DISSIPATER CONSTRUCTED OF RIPRAP OR SANDBAGS.
- WATER FROM THE WORK AREA SHALL BE PUMPED TO A SEDIMENT FILTERING MEASURE SUCH AS A SEDIMENT BAG OR OTHER APPROVED DEVICE. THE MEASURE SHALL BE LOCATED SUCH THAT THE WATER DRAINS BACK INTO THE CHANNEL BELOW THE DOWNSTREAM SANDBAG DIKE WITHOUT CAUSING EROSION BETWEEN THE SEDIMENT FILTER BAG AND THE STREAM BANK.

TEMPORARY PUMP AROUND

NCG01 GROUND STABILIZATION AND MATERIALS HANDLING

EFFECTIVE: 04/01/19

PART III SELF-INSPECTION, RECORDKEEPING AND REPORTING

SECTION A: SELF-INSPECTION

Self-inspections are required during normal business hours in accordance with the table below. When adverse weather or site conditions would cause the safety of the inspection personnel to be in jeopardy, the inspection may be delayed until the next business day on which it is safe to perform the inspection. In addition, when a storm event of equal to or greater than 1.0 inch occurs outside of normal business hours, the self-inspection shall be performed upon the commencement of the next business day. Any time when inspections were delayed shall be noted in the Inspection Record.

Inspect	Frequency (during normal business hours)	Inspection records must include:
(1) Rain gauge maintained in good working order	Daily	Daily rainfall amounts. If no daily rain gauge observations are made during weekend or holiday periods, and no individual-day rainfall information is available, record the cumulative rain measurement for those unattended days (note this will determine if a site inspection is needed). Days on which no rainfall occurred shall be recorded as "zero." The permittee may use another rain-monitoring device approved by the Division.
(2) E&S Measures	At least once per 7 calendar days and within 24 hours of a rain event ≥ 1.0 inch in 24 hours	1. Identification of the measures inspected, Date and time of the inspection, 2. Name of the person performing the inspection, 3. Indication of whether the measures were operating properly, 4. Description of maintenance needs for the measure, 5. Description, evidence, and date of corrective actions taken.
(3) Stormwater discharge outfalls (SDCs)	At least once per 7 calendar days and within 24 hours of a rain event ≥ 1.0 inch in 24 hours	1. Identification of the discharge outfalls inspected, 2. Date and time of the inspection, 3. Name of the person performing the inspection, 4. Evidence of indicators of stormwater pollution such as oil sheen, floating or suspended solids or discoloration, 5. Indication of visible sediment leaving the site, 6. Description, evidence, and date of corrective actions taken.
(4) Perimeter of site	At least once per 7 calendar days and within 24 hours of a rain event ≥ 1.0 inch in 24 hours	If visible sedimentation is found outside site limits, then a record of the following shall be made: 1. Actions taken to clean up or stabilize the sediment that has left the site limits, 2. Description, evidence, and date of corrective actions taken, and 3. An explanation as to the actions taken to control future releases.
(5) Streams or wetlands onsite or offsite (where accessible)	At least once per 7 calendar days and within 24 hours of a rain event ≥ 1.0 inch in 24 hours	If the stream or wetland has increased visible sedimentation or a stream has visible increased turbidity from the construction activity, then a record of the following shall be made: 1. Description, evidence and date of corrective actions taken, and 2. Records of the required reports to the appropriate Division Regional Office per Part III, Section C, Item 2(a) of this permit.
(6) Ground stabilization measures	After each phase of grading	1. The phase of grading (installation of perimeter E&S measures, clearing and grubbing, installation of storm drainage facilities, completion of all land-disturbing activity, construction or redevelopment, permanent ground cover), 2. Documentation that the required ground stabilization measures have been provided within the required timeframe or an assurance that they will be provided as soon as possible.

NOTE: The rain inspection resets the required 7 calendar day inspection requirement.

PART II, SECTION G, ITEM (4) DRAW DOWN OF SEDIMENT BASINS FOR MAINTENANCE OR CLOSE OUT

Sediment basins and traps that receive runoff from drainage areas of one acre or more shall use outlet structures that withdraw water from the surface when these devices need to be drawn down for maintenance or close out unless this is infeasible. The circumstances in which it is not feasible to withdraw water from the surface shall be rare (for example, times with extended cold weather). Non-surface withdrawals from sediment basins shall be allowed only when all of the following criteria have been met:

- The E&S plan authority has been provided with documentation of the non-surface withdrawal and the specific time periods or conditions in which it will occur. The non-surface withdrawal shall not commence until the E&S plan authority has approved these items.
- The non-surface withdrawal has been reported as an anticipated bypass in accordance with Part III, Section C, Item 2(c) and (d) of this permit.
- Dewatering discharges are treated with controls to minimize discharges of pollutants from stormwater that is removed from the sediment basin. Examples of appropriate controls include properly sited, designed and maintained dewatering tanks, weir tanks, and filtration systems.
- Vegetated, upland areas of the sites or a properly designed stone pad is used to the extent feasible at the outlet of the dewatering treatment devices described in item (c) above.
- Velocity dissipation devices such as check dams, sediment traps, and riprap are provided at the discharge points of all dewatering devices, and
- Sediment removed from the dewatering treatment devices described in item (c) above is disposed of in a manner that does not cause deposition of sediment into waters of the United States.

NCG01 SELF-INSPECTION, RECORDKEEPING AND REPORTING

EFFECTIVE: 04/01/19

PART III SELF-INSPECTION, RECORDKEEPING AND REPORTING

SECTION B: RECORDKEEPING

1. E&S Plan Documentation

The approved E&S plan as well as any approved deviation shall be kept on the site. The approved E&S plan must be kept up-to-date throughout the coverage under this permit. The following items pertaining to the E&S plan shall be kept on site and available for inspection at all times during normal business hours.

Item to Document	Documentation Requirements
(a) Each E&S measure has been installed and does not significantly deviate from the locations, dimensions and relative elevations shown on the approved E&S plan.	Initial and date each E&S measure on a copy of the approved E&S plan or complete, date and sign an inspection report that lists each E&S measure shown on the approved E&S plan. This documentation is required upon the initial installation of the E&S measures or if the E&S measures are modified after initial installation.
(b) A phase of grading has been completed.	Initial and date a copy of the approved E&S plan or complete, date and sign an inspection report to indicate completion of the construction phase.
(c) Ground cover is located and installed in accordance with the approved E&S plan.	Initial and date a copy of the approved E&S plan or complete, date and sign an inspection report to indicate completion of the ground cover specifications.
(d) The maintenance and repair requirements for all E&S measures have been performed.	Complete, date and sign an inspection report.
(e) Corrective actions have been taken to E&S measures.	Initial and date a copy of the approved E&S plan or complete, date and sign an inspection report to indicate the completion of the corrective action.

2. Additional Documentation to be Kept on Site

In addition to the E&S plan documents above, the following items shall be kept on the site and available for inspectors at all times during normal business hours, unless the Division provides a site-specific exemption based on unique site conditions that make this requirement not practical:

- This General Permit as well as the Certificate of Coverage, after it is received.
- Records of inspections made during the previous twelve months. The permittee shall record the required observations on the Inspection Record Form provided by the Division or a similar inspection form that includes all the required elements. Use of electronically-available records in lieu of the required paper copies will be allowed if shown to provide equal access and utility as the hard-copy records.

3. Documentation to be Retained for Three Years

All data used to complete the e-NOI and all inspection records shall be maintained for a period of three years after project completion and made available upon request. [40 CFR 122.41]

PART III SELF-INSPECTION, RECORDKEEPING AND REPORTING

SECTION C: REPORTING

1. Occurrences that Must be Reported

- Permittees shall report the following occurrences:
- Visible sediment deposition in a stream or wetland.
 - Oil spills if:
 - They are 25 gallons or more,
 - They are less than 25 gallons but cannot be cleaned up within 24 hours,
 - They cause sheen on surface waters (regardless of volume), or
 - They are within 100 feet of surface waters (regardless of volume).
 - Releases of hazardous substances in excess of reportable quantities under Section 311 of the Clean Water Act (Ref: 40 CFR 110.3 and 40 CFR 117.3) or Section 102 of CERCLA (Ref: 40 CFR 302.4) or G.S. 143-215.85.
 - Anticipated bypasses and unanticipated bypasses.
 - Noncompliance with the conditions of this permit that may endanger health or the environment.

2. Reporting Timeframes and Other Requirements

After a permittee becomes aware of an occurrence that must be reported, he shall contact the appropriate Division regional office within the timeframes and in accordance with the other requirements listed below. Occurrences outside normal business hours may also be reported to the Department's Environmental Emergency Center personnel at (800) 858-0368.

Occurrence	Reporting Timeframes (After Discovery) and Other Requirements
(a) Visible sediment deposition in a stream or wetland	- Within 24 hours, an oral or electronic notification. - Within 7 calendar days, a report that contains a description of the sediment and actions taken to address the cause of the deposition. Division staff may waive the requirement for a written report on a case-by-case basis.
(b) Oil spills and release of hazardous substances per item 3.(b)-(c) above	Within 24 hours, an oral or electronic notification. The notification shall include information about the date, time, nature, volume and location of the spill or release.
(c) Anticipated bypasses (40 CFR 122.41(m)(3))	A report at least ten days before the date of the bypass, if possible. The report shall include an evaluation of the anticipated quality and effect of the bypass.
(d) Unanticipated bypasses (40 CFR 122.41(m)(3))	- Within 24 hours, an oral or electronic notification. - Within 7 calendar days, a report that includes an evaluation of the quality and effect of the bypass.
(e) Noncompliance with the conditions of this permit that may endanger health or the environment (40 CFR 122.41(f)(7))	- Within 24 hours, an oral or electronic notification. - Within 7 calendar days, a report that contains a description of the noncompliance, and its causes; the period of noncompliance, including exact dates and times, and if the noncompliance has not been corrected, the anticipated time noncompliance is expected to continue; and steps taken or planned to reduce, eliminate, and prevent recurrence of the noncompliance. (40 CFR 122.41(f)(8)). - Division staff may waive the requirement for a written report on a case-by-case basis.



Date:

Page:

NON-INVASIVE PERMANENT SEEDING RECOMMENDATIONS FOR LATE WINTER AND EARLY SPRING

Species	Rate
Centipede	5 lbs/acre
Indian Woodoats	1.5-2.5 lbs/acre*
Virginia Wild Rye	4-6 lbs/acre*

*Depending upon mix with other species. See table 6.11.d from Chapter 6 of the NC Erosion and Sediment Control Planning and Design Manual.

Seeding Dates

Coastal or Eastern Piedmont for Centipede- Sept. 1 - May 1
Coastal and Piedmont for Indian Woodoats and Virginia Wild Rye- Feb 15 - April 1
Mountains for Indian Woodoats and Virginia Wild Rye- March 1 - May 15

Maintenance:

Significant maintenance may be required to obtain desired cover once centipede is planted. Acceptable for sodding.

NON-INVASIVE PERMANENT SEEDING RECOMMENDATIONS FOR SUMMER

Species	Rate
Indian Woodoats	1.5-2.5 lbs/acre*
Virginia Wild Rye	4-6 lbs/acre*

*Depending upon mix with other species. See table 6.11.d from Chapter 6 of the NC Erosion and Sediment Control Planning and Design Manual.

Seeding Dates

Mountains - July 15- Aug 15
Piedmont - Aug 15 - Oct 15

Maintenance:

Indian Woodoats and Virginia Wild Rye are both sun and shade tolerant.

SEED BED PREPARATION:

LIMING- Apply lime according to soil test recommendations. If the pH (acidity) of the soil is not known, an application of ground agricultural limestone at the rate of 1 to 1 1/2 tons/acre on coarse-textured soils and 2-3 tons/acre on fine-textured soils is usually sufficient. Apply limestone uniformly and incorporate into the top 4-6 inches of soil. Soils with a pH of 6 or higher need not be limed.

FERTILIZER- Base application rates on soil tests. When these are not possible, apply a 10-10-10 grade fertilizer at 700-1,000 lb/acre. Both fertilizer and lime should be incorporated into the top 4-6 inches of soil. If a hydraulic seeder is used, do not mix seed and fertilizer more than 30 minutes before application.

SURFACE ROUGHENING- If recent tillage operations have resulted in a loose surface additional roughening may not be required, except to break up large clods. If rainfall causes the surface to become sealed or crusted, loosen it just prior to seeding by raking, harrowing, or other suitable methods for fine grading. The finished grade shall be a smooth even soil surface with a loosen uniformly fine texture. All ridges and depressions shall be removed and filled to provide the approved surface drainage. Planting is to be done immediately after finished grades are obtained and seedbed preparation is completed.

NOTES:

- Permanent seeding, sodding or other means of stabilization are required when all construction work is completed according to the NPDES timeframe's table.
- A North Carolina Department of Agriculture soils test (or equal) is highly recommended to be obtained for all areas to be seeded, sprigged, sodded or planted.
- Use a seeding mix that will produce fast growing nurse crops and includes non-invasive species that will eventually provide a permanent groundcover. Soil blankets may be used in lieu of nurse crops. Mat, tack or crimp mulch, as needed to stabilize seeded areas until root establishment. Mulch must be applied uniformly over the soil with a cover density of at least 80%.
- Ground cover shall be maintained until permanent vegetation is established and stable against accelerated erosion.



PERMANENT SEEDING RECOMMENDATIONS



REVISION:

NO.	DATE	REVISION

STIPULATION FOR REUSE

THIS DRAWING WAS PREPARED FOR USE ON THE SPECIFIC SITE, NAMED HEREON, CONTEMPORANEOUSLY WITH ITS ISSUE DATE AS LISTED, HEREON, AND IT IS NOT SUITABLE FOR USE ON A DIFFERENT PROJECT SITE OR AT A LATER TIME. USE OF THIS DRAWING FOR REFERENCE OR EXAMPLE ON ANOTHER PROJECT REQUIRES THE SERVICES OF PROPERLY LICENSED ARCHITECTS AND ENGINEERS. REPRODUCTION OF THIS DRAWING FOR REUSE ON ANOTHER PROJECT IS NOT AUTHORIZED AND MAY BE CONTRARY TO THE LAW.

MERRITT RESERVE

EROSION CONTROL DETAILS

ROLESVILLE RD

WAKE COUNTY NC 27312

JOB NUMBER: 23-0004

CHECKED BY: JK

DRAWN BY: DH/MA/LL

DATE: 12/12/2025

SHEET TITLE:

EROSION CONTROL DETAILS

SHEET NO.:

CE-503



*** 3 Days Before Digging ***
North Carolina 811
811 or 1-800-632-4969
Remote Ticket Entry
http://nc811.org/remoteticketentry.htm

PROJECT NUMBER = CID-25-02

SHEET NO.: **CE-504**
